


RAILWEAVE: ONE AXIS, THREE CORRIDORS, THREE HUBS

REGIONAL CHAIN | CORRIDOR WEAVE | PLACE-BASED PROJECTS | PROBLEM—VALIDATION—FIRST USE—KNOWLEDGE RETURN

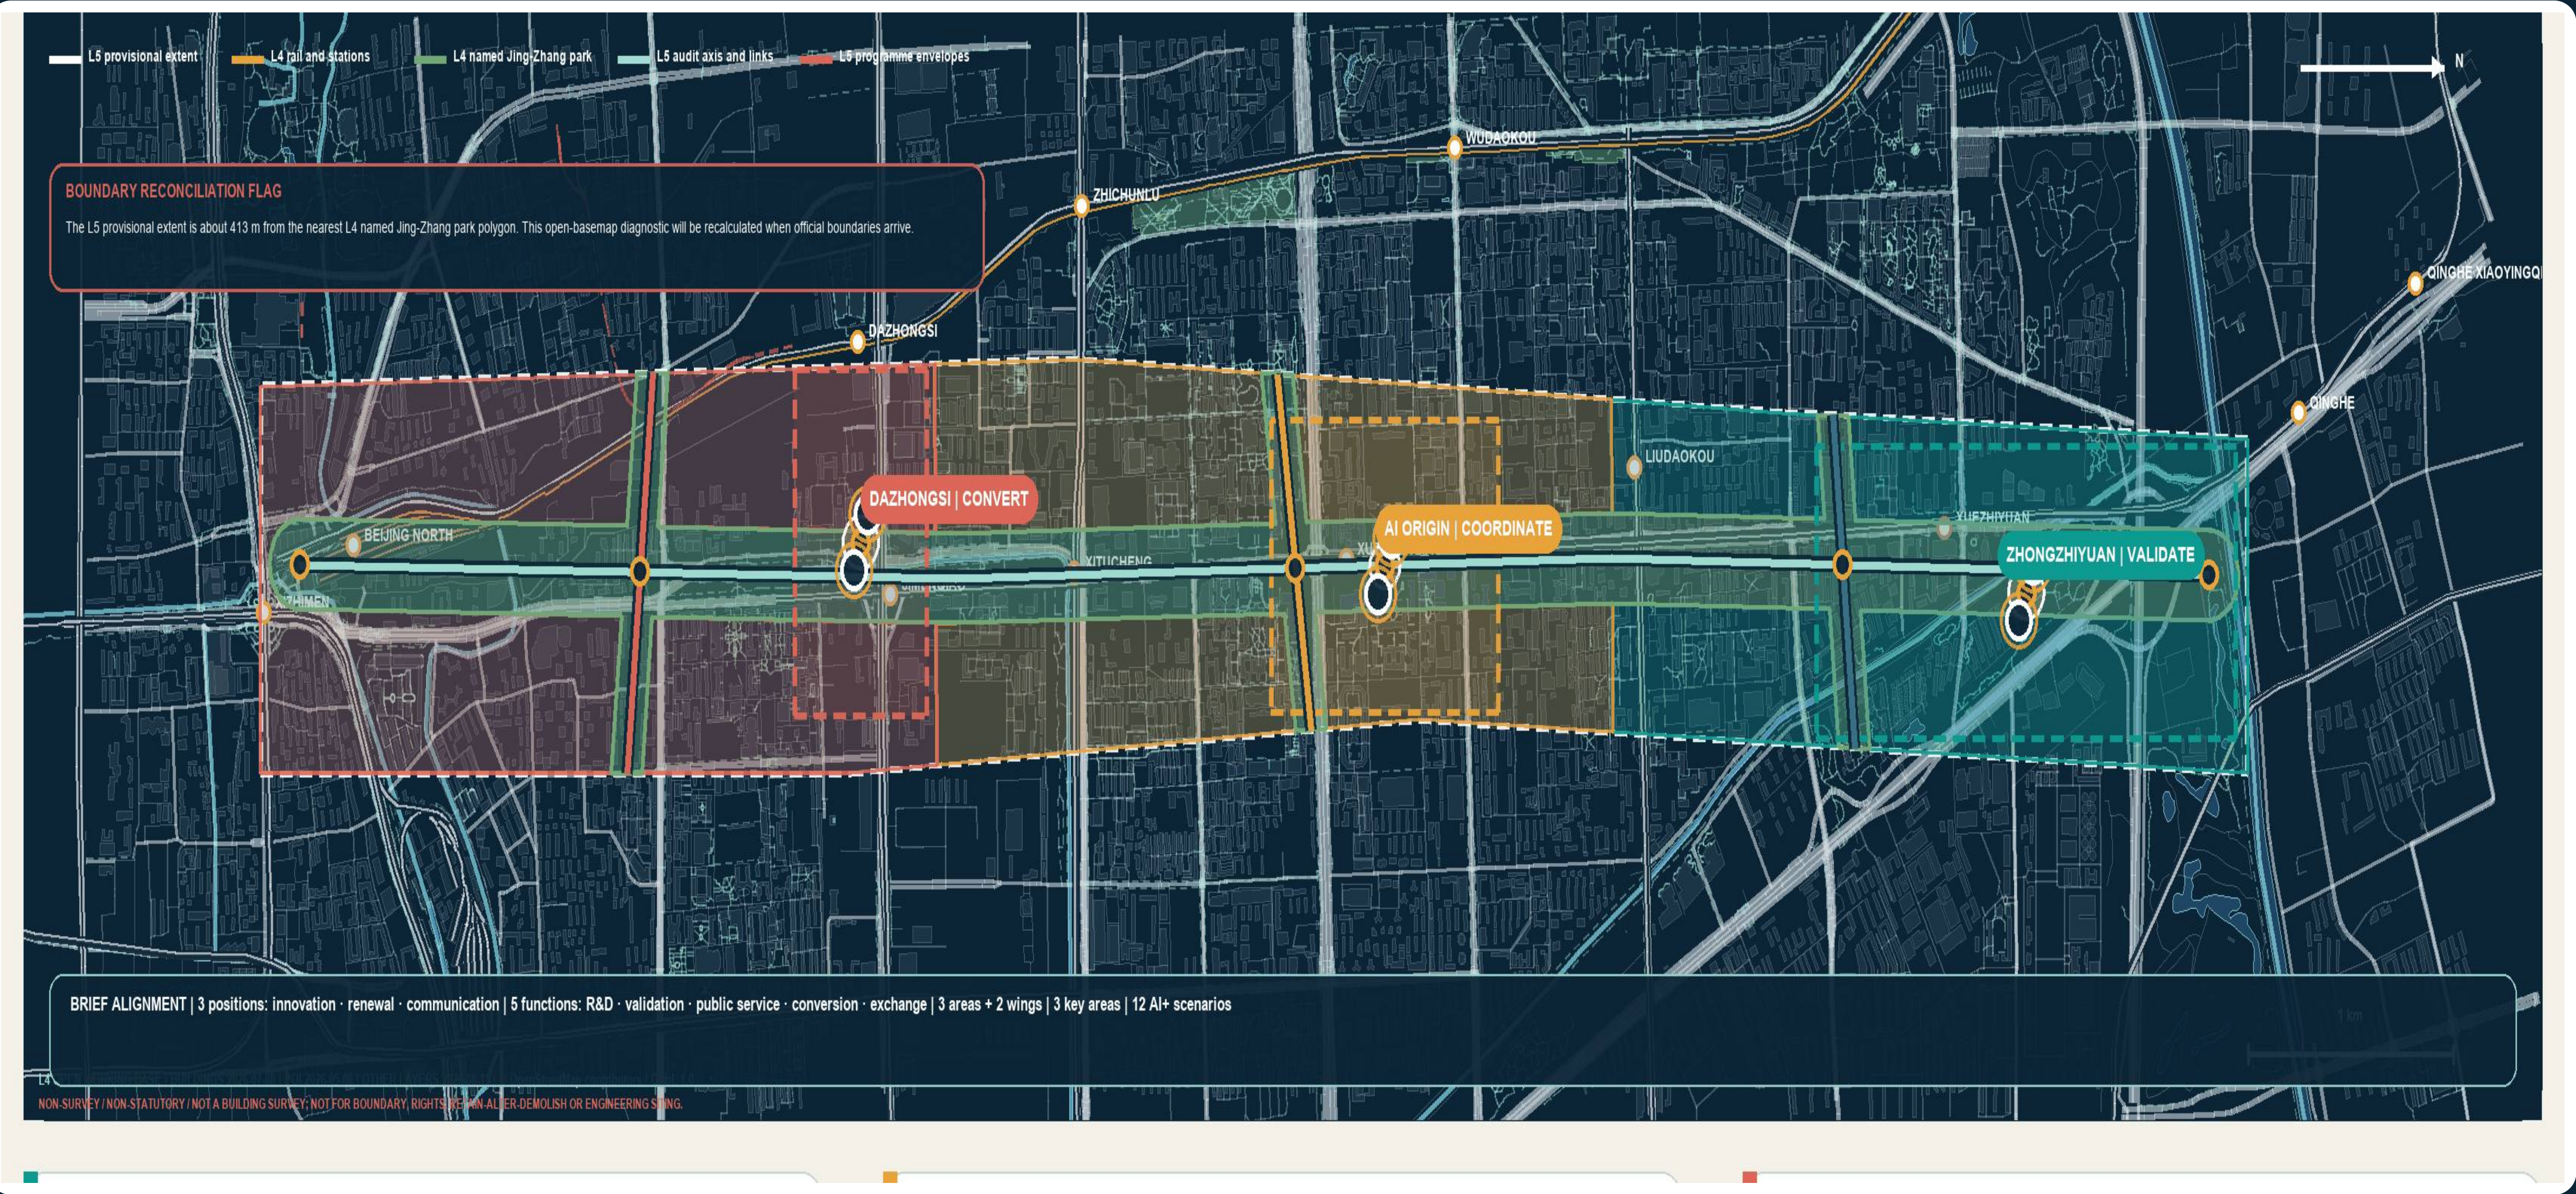

THREE PLACE-BASED PROJECTS

- 01 ZHONGZHIYUAN | OBSERVABLE VALIDATION YARD
- 02 AI ORIGIN | OPEN REPAIR STREET
- 03 DAZHONGSI | FIRST-USE SERVICE CONCOURSE

FIRST ACTION | 100-DAY BOUNDED TEST AT AI ORIGIN OPEN REPAIR STREET

PUBLICLY VERIFIABLE | ORIGIN BUILDING GROUND FLOOR: 1,650 m² EXISTING FIT-OUT PROJECT, PERMIT, JOINT ACCEPTANCE, ONE ORGANISED VISIT ON 29 JULY 2026

BEFORE ADVANCE | WRITTEN SITE CONSENT, FIELD REVIEW, ORDINARY-SERVICE BASELINE, DUTY RECEIPT, S06 QUANTITIES AND PROJECT QUOTES

0-10	11-30	31-45	46-60	61-90	91-100
SITE	BASELINE	COST+DUTY	CLOSED TEST	BOUNDED USE	RESTORE+DECIDE

P04 / THREE PLACE-BASED PLAN-SECTION-OPERATION PROTOTYPES

Three Key Areas: Context Plan, Spatial Experience, Delivery Interface and Responsibility Acceptance

Each area uses an L4 open basemap for real urban context and L5 provisional geometry for design tasks; concept images are not evidence of baseline, buildings, engineering or investment.

01

ZHONGZHIYUAN

CONTROLLED VALIDATION


L4 CONTEXT + L5 STUDY PLAN

E ENTRY | P1 PRIMARY | P2 SECONDARY | S1 SERVICE/EMERGENCY | Z1-Z4 ZONES | V1 VIEW



L4 OPEN WORKING BASE | BUILDINGS 2026-07-00 | POI 2026-05-06 | OTHER LAYERS 2026-05-06 | © OpenStreetMap contributors / ODbL 1.0
NON-SURVEY / NON-STATUTORY / NOT A BUILDING SURVEY; NOT FOR BOUNDARY, RIGHTS, REMAIN AFTER DEMOLISH OR ENGINEERING SITING.

AI CONCEPT / NOT BASELINE

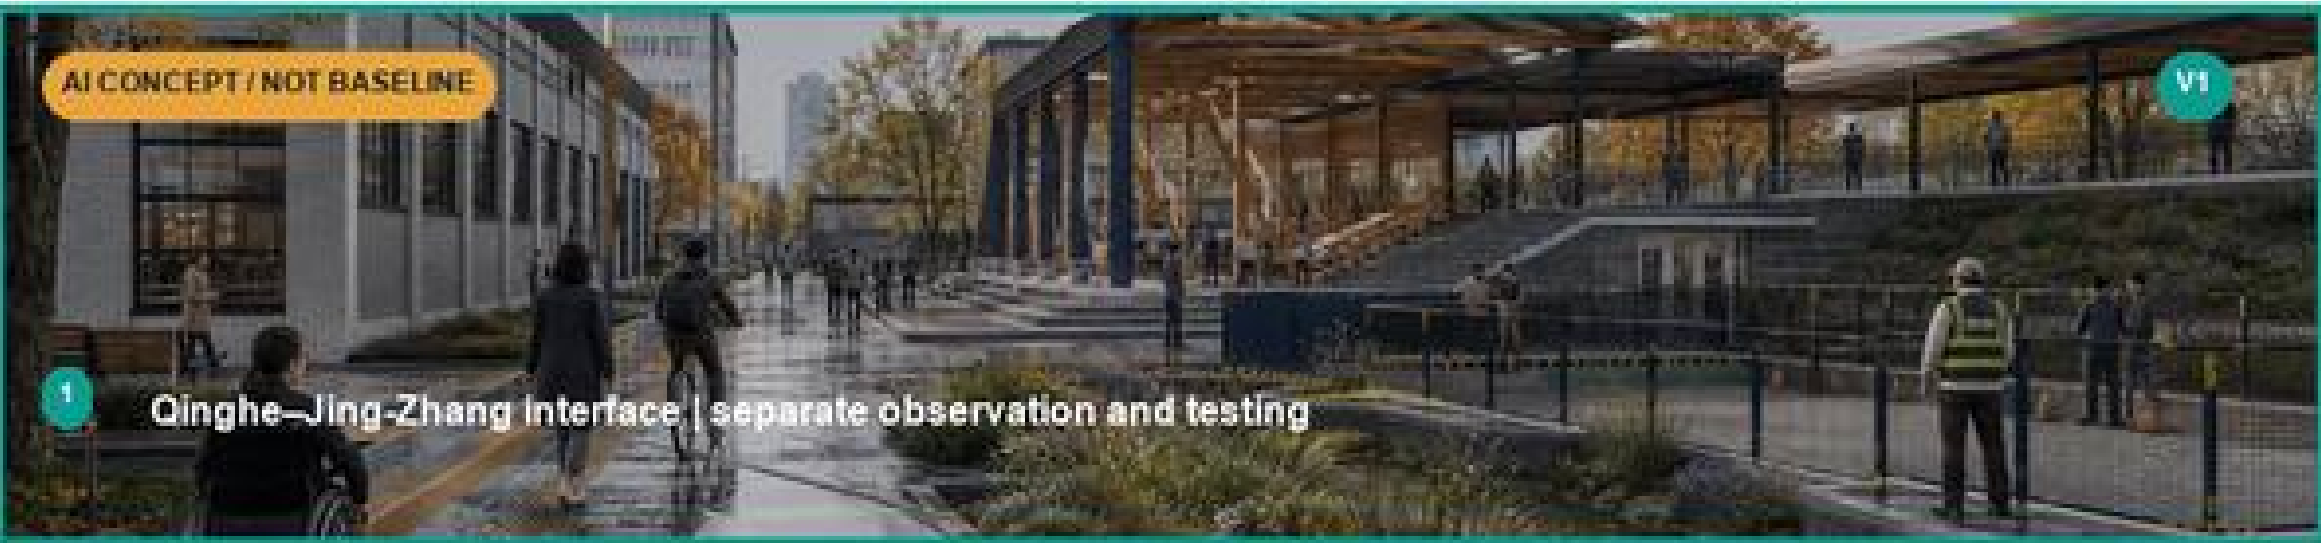

1 Qinghe-Jing-Zhang Interface | separate observation and testing

2 AN-V21-007 + ZY-AA/BB | opening, access, isolation and emergency pending

3 DC/PC-ZY-001/002 | removable and restorable; stop if rights/fire/insurance remain open

RESPONSIBILITY AND ACCEPTANCE

Lawfully appoint IE, IV and DC and obtain written receipt; validation remains separate from operations.

ROLE ARCHETYPE → LAWFUL APPOINTMENT → WRITTEN RECEIPT

DIMENSIONS, RIGHTS, ENTRANCES, CONTROL LINES, BUILDINGS AND ENGINEERING ALL REQUIRE FORMAL REVIEW

02

AI ORIGIN

DEMAND COORDINATION

L4 CONTEXT + L5 STUDY PLAN

E ENTRY | P1 PRIMARY | P2 SECONDARY | S1 SERVICE/EMERGENCY | Z1-Z4 ZONES | V1 VIEW



L4 OPEN WORKING BASE | BUILDINGS 2026-07-00 | POI 2026-05-06 | OTHER LAYERS 2026-05-06 | © OpenStreetMap contributors / ODbL 1.0
NON-SURVEY / NON-STATUTORY / NOT A BUILDING SURVEY; NOT FOR BOUNDARY, RIGHTS, REMAIN AFTER DEMOLISH OR ENGINEERING SITING.

AI CONCEPT / NOT BASELINE



1 University-community-campus network | shared ground floor retains staffed ordinary service

2 AN-V21-005 + AI-AA/BB | floor, rights, fire and hours pending

3 DC/PC-AI-001/002 | movable and pausable; paper/phone/staff remain available

RESPONSIBILITY AND ACCEPTANCE

Lawfully appoint IE, DO and PO and obtain written receipt; refusing AI adds no charge, unreasonable wait or off-site trip.

ROLE ARCHETYPE → LAWFUL APPOINTMENT → WRITTEN RECEIPT

DIMENSIONS, RIGHTS, ENTRANCES, CONTROL LINES, BUILDINGS AND ENGINEERING ALL REQUIRE FORMAL REVIEW

03

DAZHONGSI

FIRST-USE CONVERSION

L4 CONTEXT + L5 STUDY PLAN

E ENTRY | P1 PRIMARY | P2 SECONDARY | S1 SERVICE/EMERGENCY | Z1-Z4 ZONES | V1 VIEW



L4 OPEN WORKING BASE | BUILDINGS 2026-07-00 | POI 2026-05-06 | OTHER LAYERS 2026-05-06 | © OpenStreetMap contributors / ODbL 1.0
NON-SURVEY / NON-STATUTORY / NOT A BUILDING SURVEY; NOT FOR BOUNDARY, RIGHTS, REMAIN AFTER DEMOLISH OR ENGINEERING SITING.

AI CONCEPT / NOT BASELINE



1 Dazhongsi surface station edge-demand compliance interface | no assumed underpass

2 AN-V21-003 + DZS-AA/BB | re-anchored to named station clue; entrances and peak flow pending

3 DC/PC-DZS-001/002 | day-90/180 review; stop if demand/budget/procurement/exit remain open

RESPONSIBILITY AND ACCEPTANCE

Lawfully appoint DO, PF and IE and obtain written receipt; renew, correct or exit with receipts.

ROLE ARCHETYPE → LAWFUL APPOINTMENT → WRITTEN RECEIPT

DIMENSIONS, RIGHTS, ENTRANCES, CONTROL LINES, BUILDINGS AND ENGINEERING ALL REQUIRE FORMAL REVIEW

CONCEPTUAL RECOMMENDATION | PROVISIONAL WORKING EXTENT | NOT FOR CONSTRUCTION | 2026-08-12

RAILWEAVE / 02

P01 / DELIVERY LEDGER

Project Gates, Responsibility and Five-Year Operating Account

A project does not advance while site, demand, data, funding, procurement, acceptance, operations or exit responsibility remains unresolved.



RW-A01

AI Origin Demand Room

Input

problem evidence pack

Acceptance artifact

demand brief + response

Stop condition

unclear demand / rights

RW-B01

Zhongzhiyuan Validation Lab

Input

version + test brief

Acceptance artifact

reproducible pack + review

Stop condition

major risk unresolved

RW-C01

Dazhongsì First-Use Operations Pool

Input

demand + validation + WLC cost

Acceptance artifact

launch list + post-review

Stop condition

procurement / OPEX unaffordable

S06 | 100-DAY BOUNDED DELIVERY: FOUR PHASES, SIX DECISION WINDOWS

P1 | DAYS 0–30

SITE + BASELINE

Days 0–10 site checks; Days 11–30 route, ordinary-service and staff baseline.

stop if rights, access, or ordinary service remains open

P2 | DAYS 31–60

COST + CLOSED TEST

Days 31–45 quantities, quotes, duty; Days 46–60 shadow log and restoration drill

return on data, takeover, or restoration failure

P3 | DAYS 61–90

BOUNDED CO-TEST

time-limited co-test after lawful authority; mandatory close-out and exit handoff on Day 90

do not start without authority; pause on a serious event

P4 | DAYS 91–100

RESTORE + DECIDE

revoke, delete, remove, restore signs and staffed service; issue one of four written opinions

no next phase if any of six exit receipts is missing

HANDOFF: role archetype → lawful appointment → written IE/DO/PO/IV receipt as applicable; exit resources are itemised, with no fixed percentage.

FIVE-YEAR COST EVIDENCE TC5

C0 + Σ(Ot + Mt + Pt + Vt + At + Rt) + U + X

G0

verify quantities and service volumes

PENDING

G1

real demand, non-AI baseline and staff

BASELINE

G4

lawful price search, market research or inquiry

UNPRICED

G4+

budget approval, effective contract or funds received

NOT SECURED

10 evidence categories: premises | equipment | staff | accessibility/ordinary service | validation | participation | insurance/emergency | maintenance | renewal | exit/restoration

Items with unverified quantity, price, responsibility or scope stay outside any firm total.


CONCEPTUAL RECOMMENDATION | PROVISIONAL WORKING EXTENT | NOT FOR CONSTRUCTION | 2026-08-12

RAILWEAVE / 03

P02 / PROGRAMME ENVELOPES ON CONTEXT

Programme Envelopes and Reversible Components: Gated Siting in the Existing Urban Fabric

Four programmes express action tasks and six components express candidate indexes only; none changes statutory land use or assumes building decisions, development intensity or build scale.

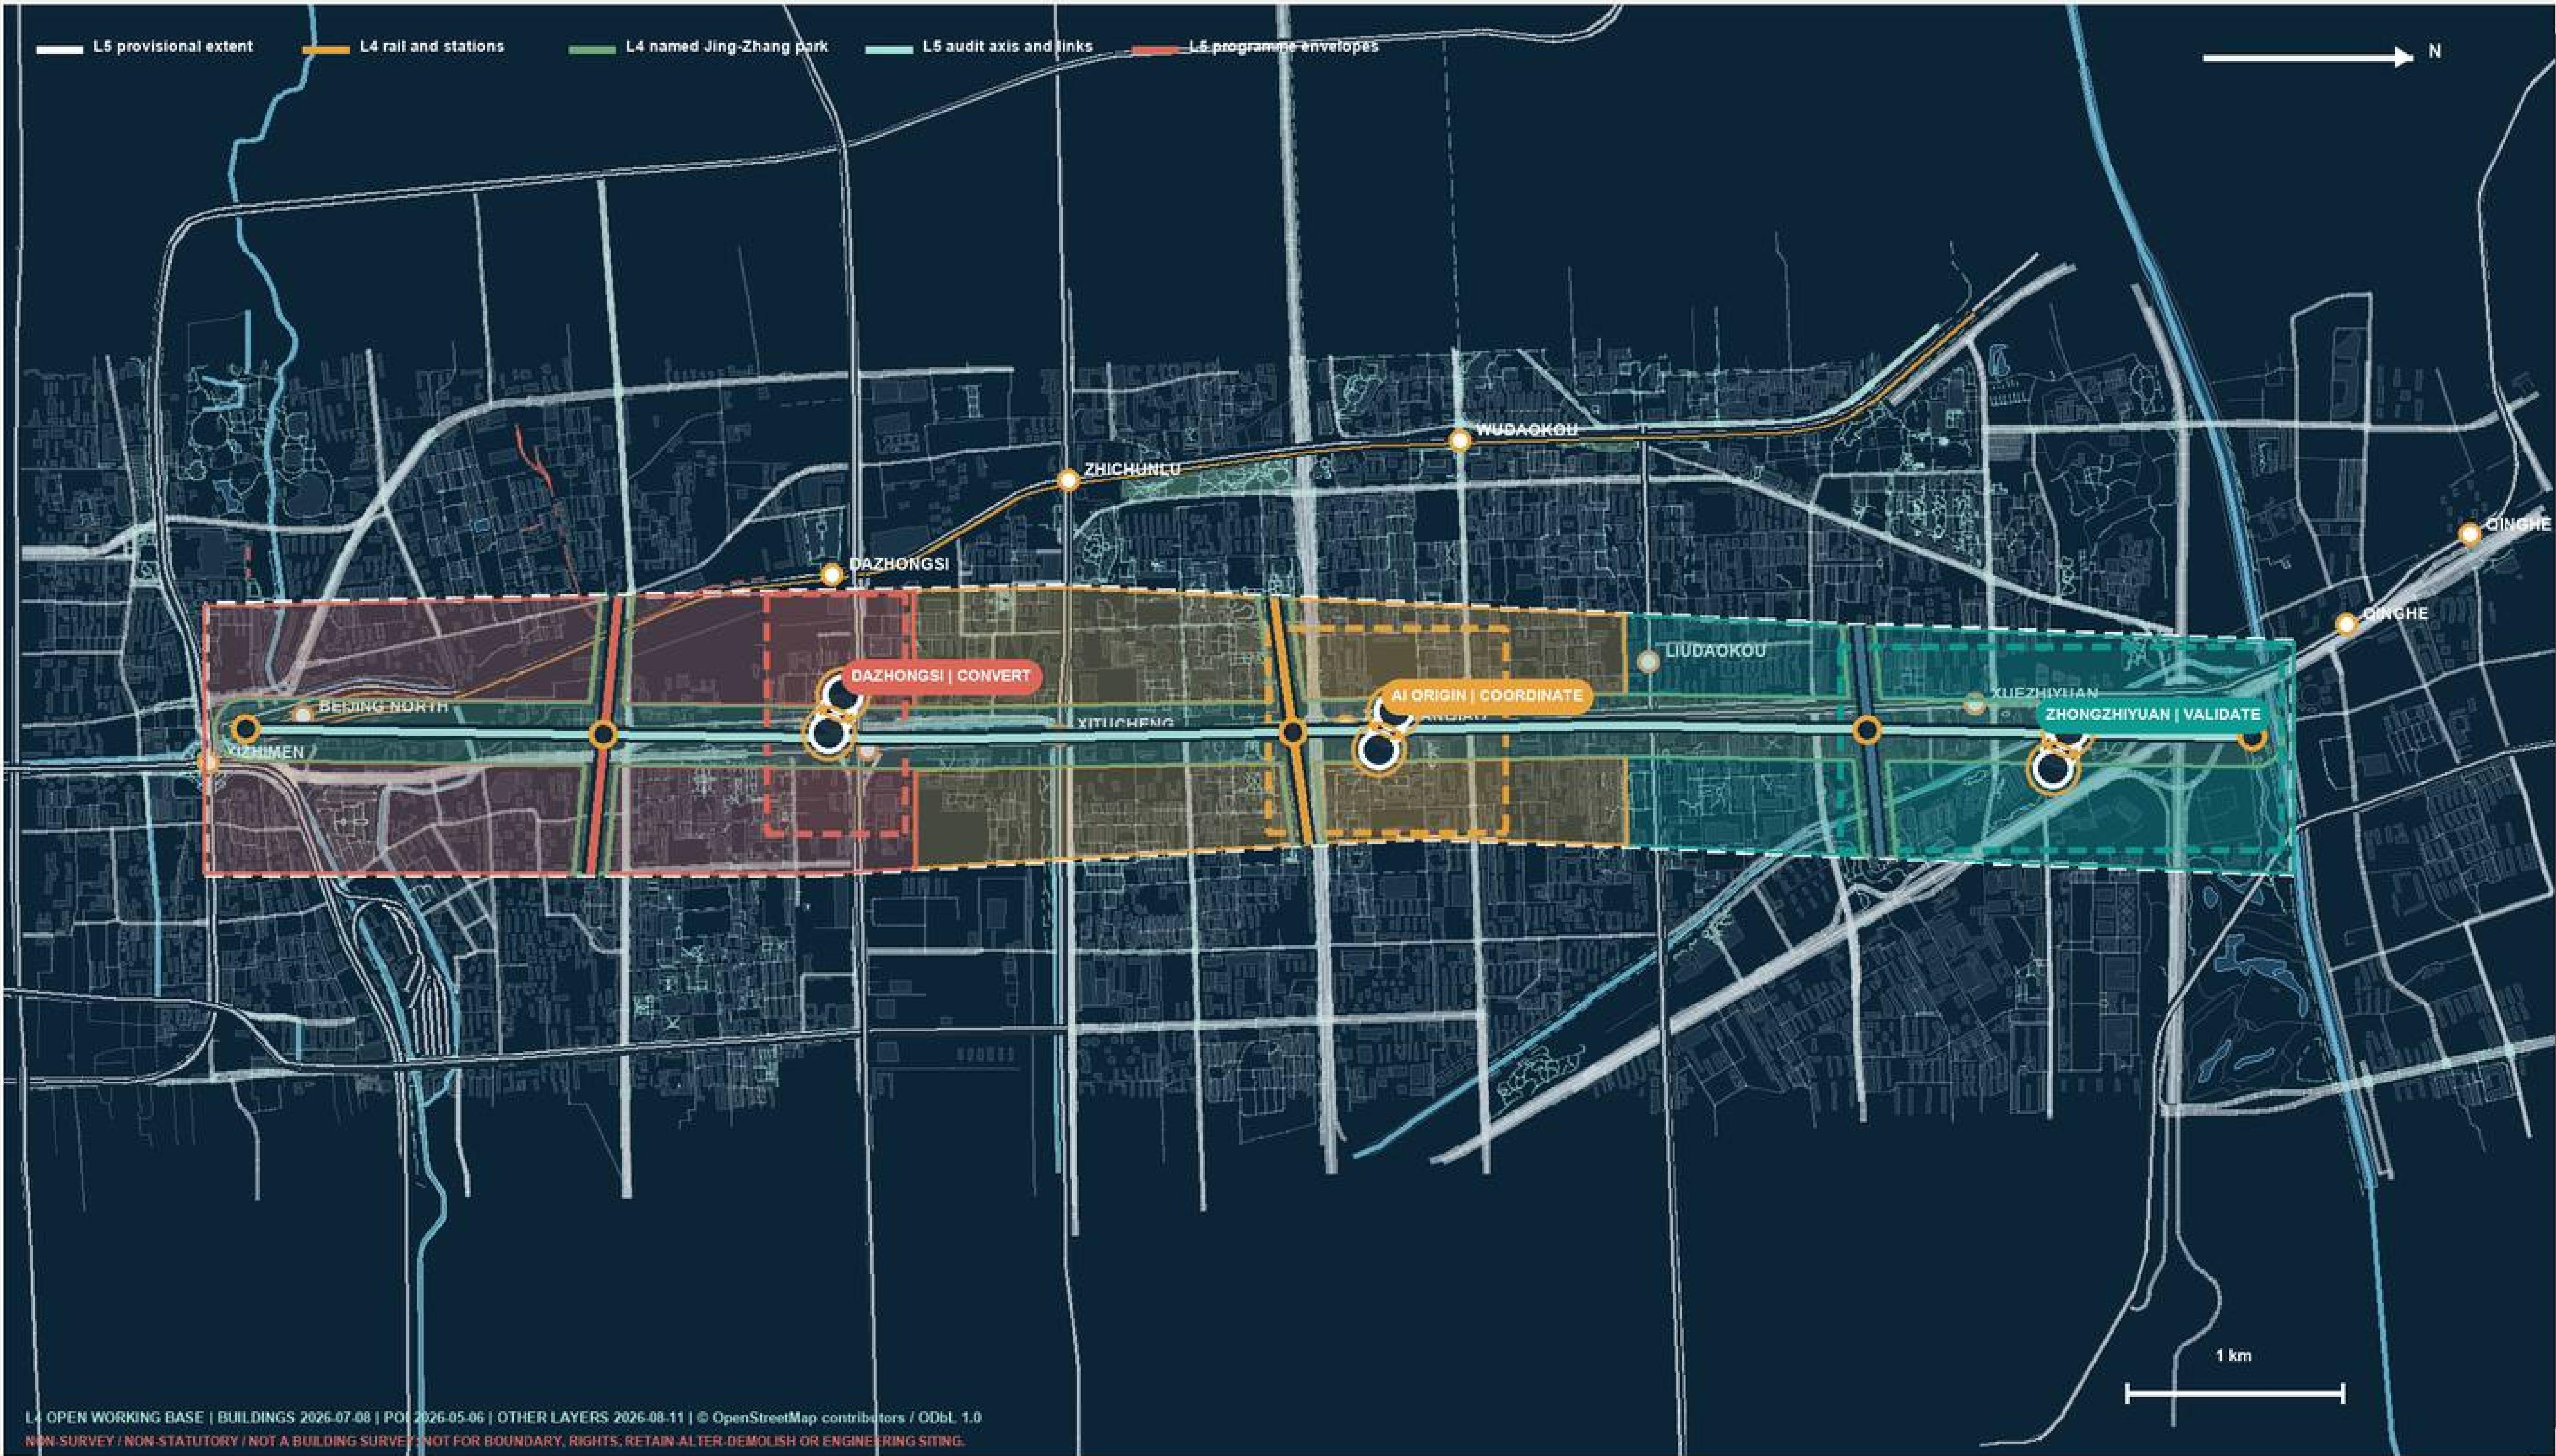

01

Open validation & R&D
Zhongzhiyuan: public observation, controlled testing, independent finding

L5 ACTION ENVELOPE | LAND USE AND RIGHTS PENDING

02

Near-campus learning & talent
AI Origin: shared ground floor, ordinary service, distributed coordination

L5 ACTION ENVELOPE | LAND USE AND RIGHTS PENDING

03

First-use & composite service
Dazhongs: real demand, lawful procurement, review and exit

L5 ACTION ENVELOPE | LAND USE AND RIGHTS PENDING

04

Public axis & blue-green links
Nine segments and eight anchors, no continuous-open claim before verification

L5 ACTION ENVELOPE | LAND USE AND RIGHTS PENDING

COMPONENT SITING ORDER

task → study window → component candidate → G0 site/rights → G1 demand/public → G2 controlled prototype

If any statutory or professional condition remains open, keep the component movable, pausable and withdrawable.

P03 / ACCESS, RAIL AND BLUE-GREEN AUDIT

Jing-Zhang Public Axis and Three Cross-Links: Nine Segments, Eight Anchors and Six Field Tests

L4 road, walking, cycling, rail, station and water leads are overlaid with L5 audit tasks; coloured lines and points do not establish opening, compliance or engineering alignment.



SIX TESTS PER SEGMENT

01

Opening & barriers

date, hours, detour

02

Step-free continuity

slope, width, steps, lift

03

Walk, cycle & crossing

conflict, wait, help

04

Rail & waterside

protection, control, flood

05

Night & emergency

lighting, patrol, emergency access

06

Operations & exit

duty, restoration, receipt


PRECONDITION FOR VERIFIED METRICS

field record + affected-user review + professional opinion + accountable receipt; every segment remains unverified beforehand.


D01 / OVERALL URBAN DESIGN WORKING PLAN

One Axis, Three Corridors, Three Hubs: Spatial Structure and Project Loop on One Review Plate

Spatial links, key areas and project gates share one identifier system; mapped relationships are working proposals, not statutory roads, waterways, land use or construction plans.

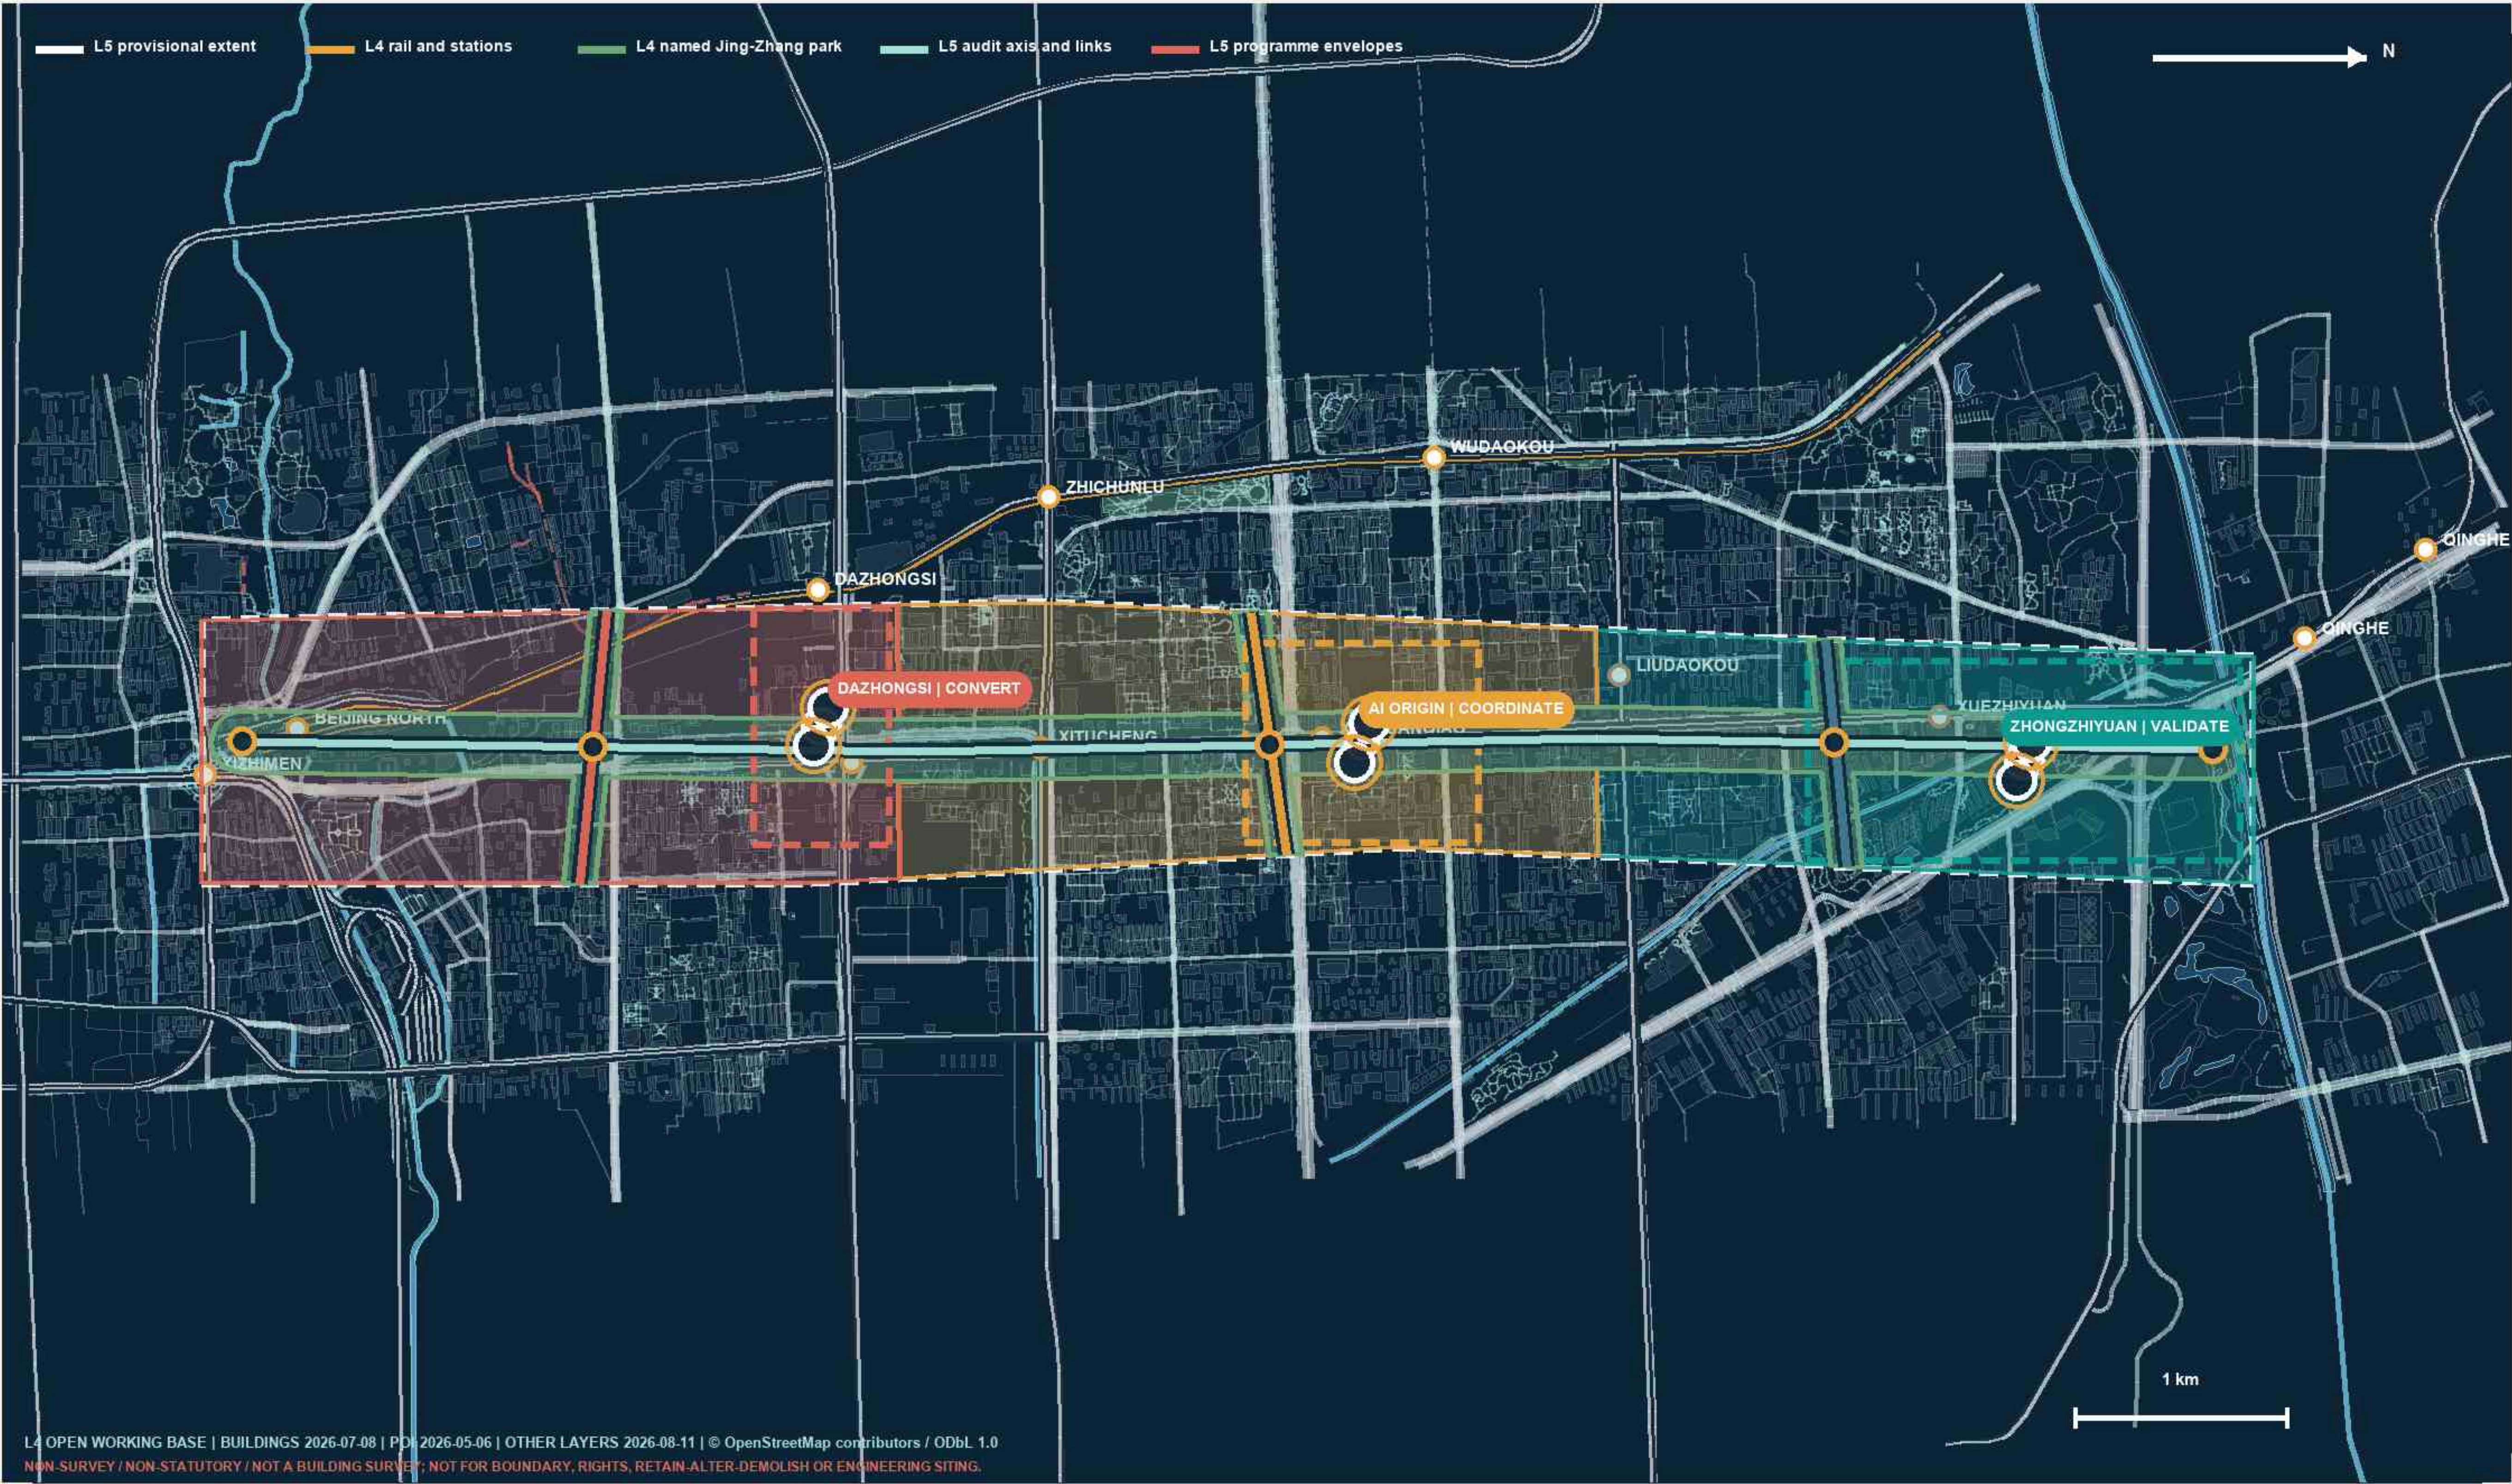

THREE-CHAIN PROJECT LOOP

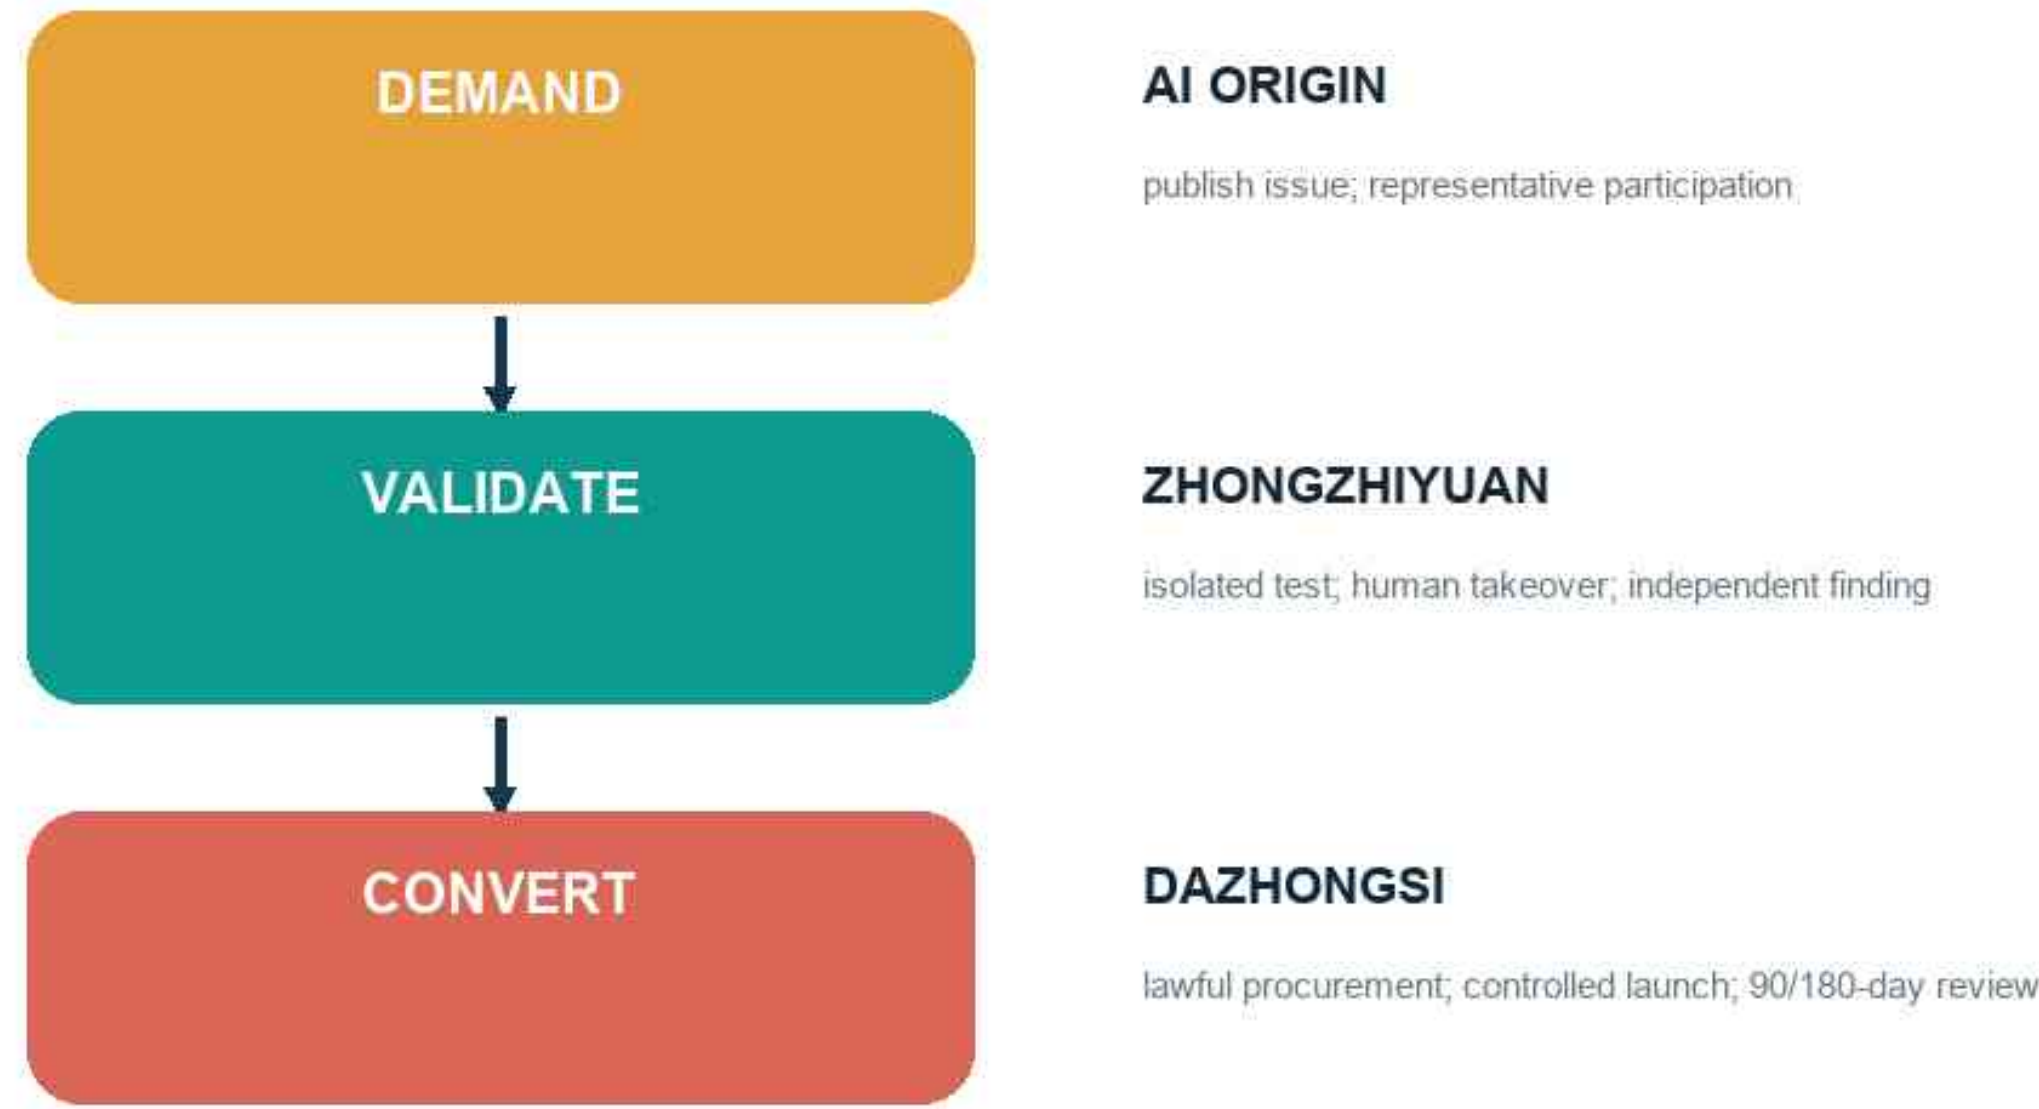

BRIEF ALIGNMENT

- 3 positions**: innovation, renewal, communication
- 5 functions**: R&D, validation, public service, conversion, exchange
- 3 areas + 2 wings**: three differentiated hubs with cross-axis inputs and outputs
- 3 key areas**: L4 context + L5 plan + AA/BB sections + delivery register
- AI+ scenarios**: 12 scenarios, dual gates, human final review and exit restoration

C1 / KEY-AREA PLAN-SECTION-OPERATION




Zhongzhiyuan · Controlled Validation System

Four zones—public observation, semi-controlled validation, controlled testing, and service/emergency—prioritising verified indoor reuse.



MAPPED OBJECTS AND REVIEW INTERFACES


WINDOW	KEY-001
AUDIT	AN-007
SECTION	SEC-ZY-AA / SEC-ZY-BB
COMPONENT	DC-ZY-001 / DC-ZY-002
PLAN ACTIONS	E1/E2/ES + P1/P2/S1 + Z1-Z4 + VIEW

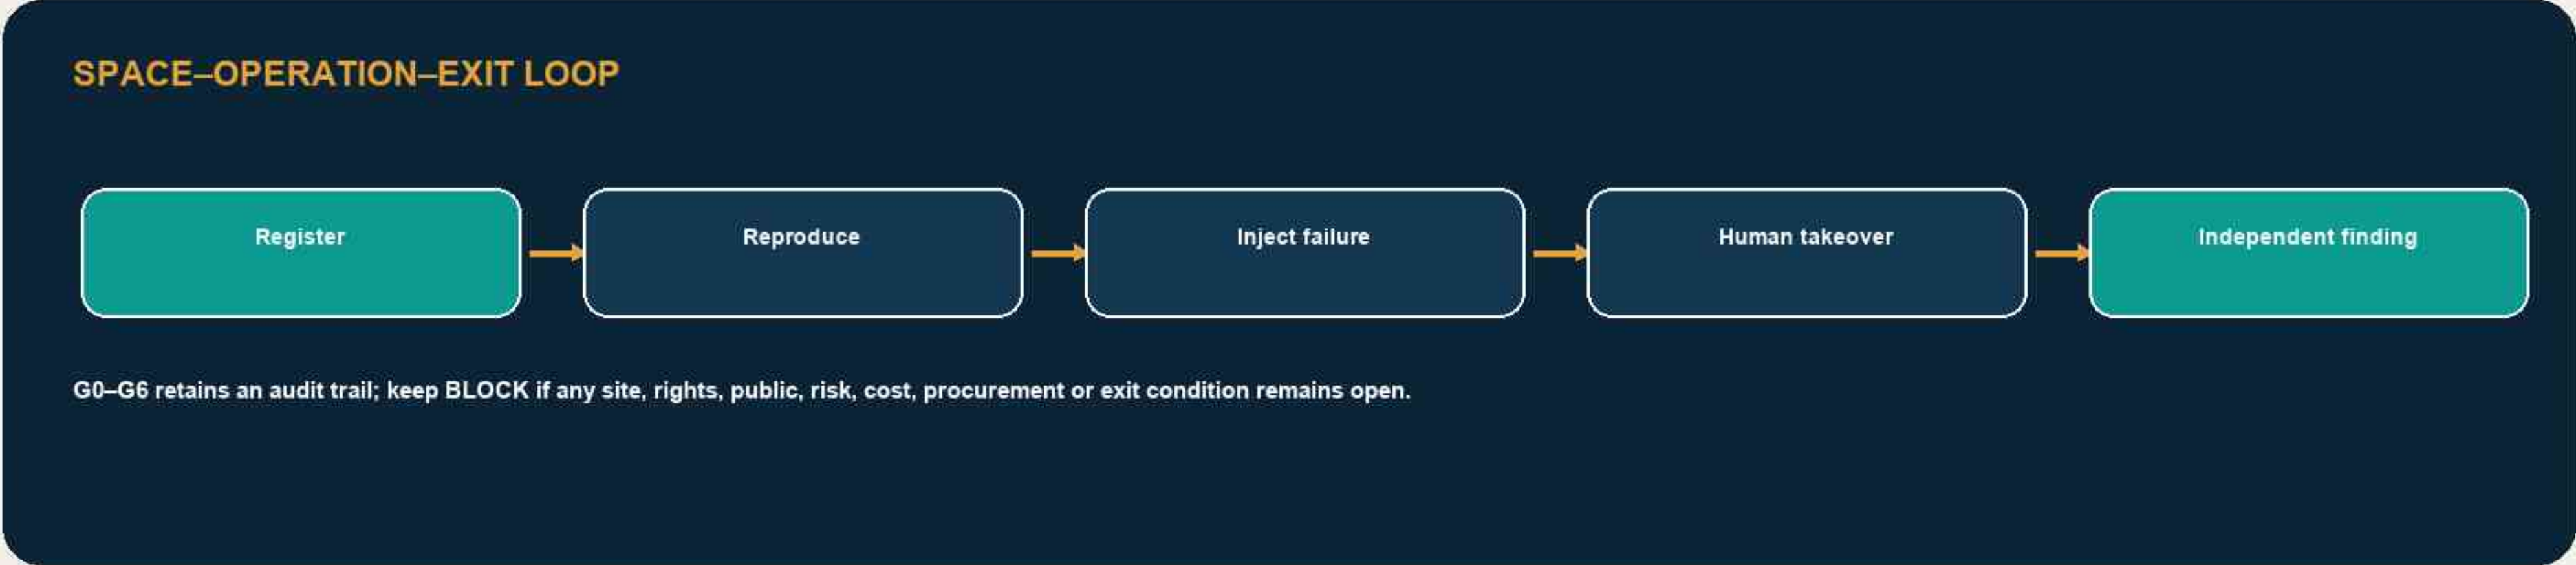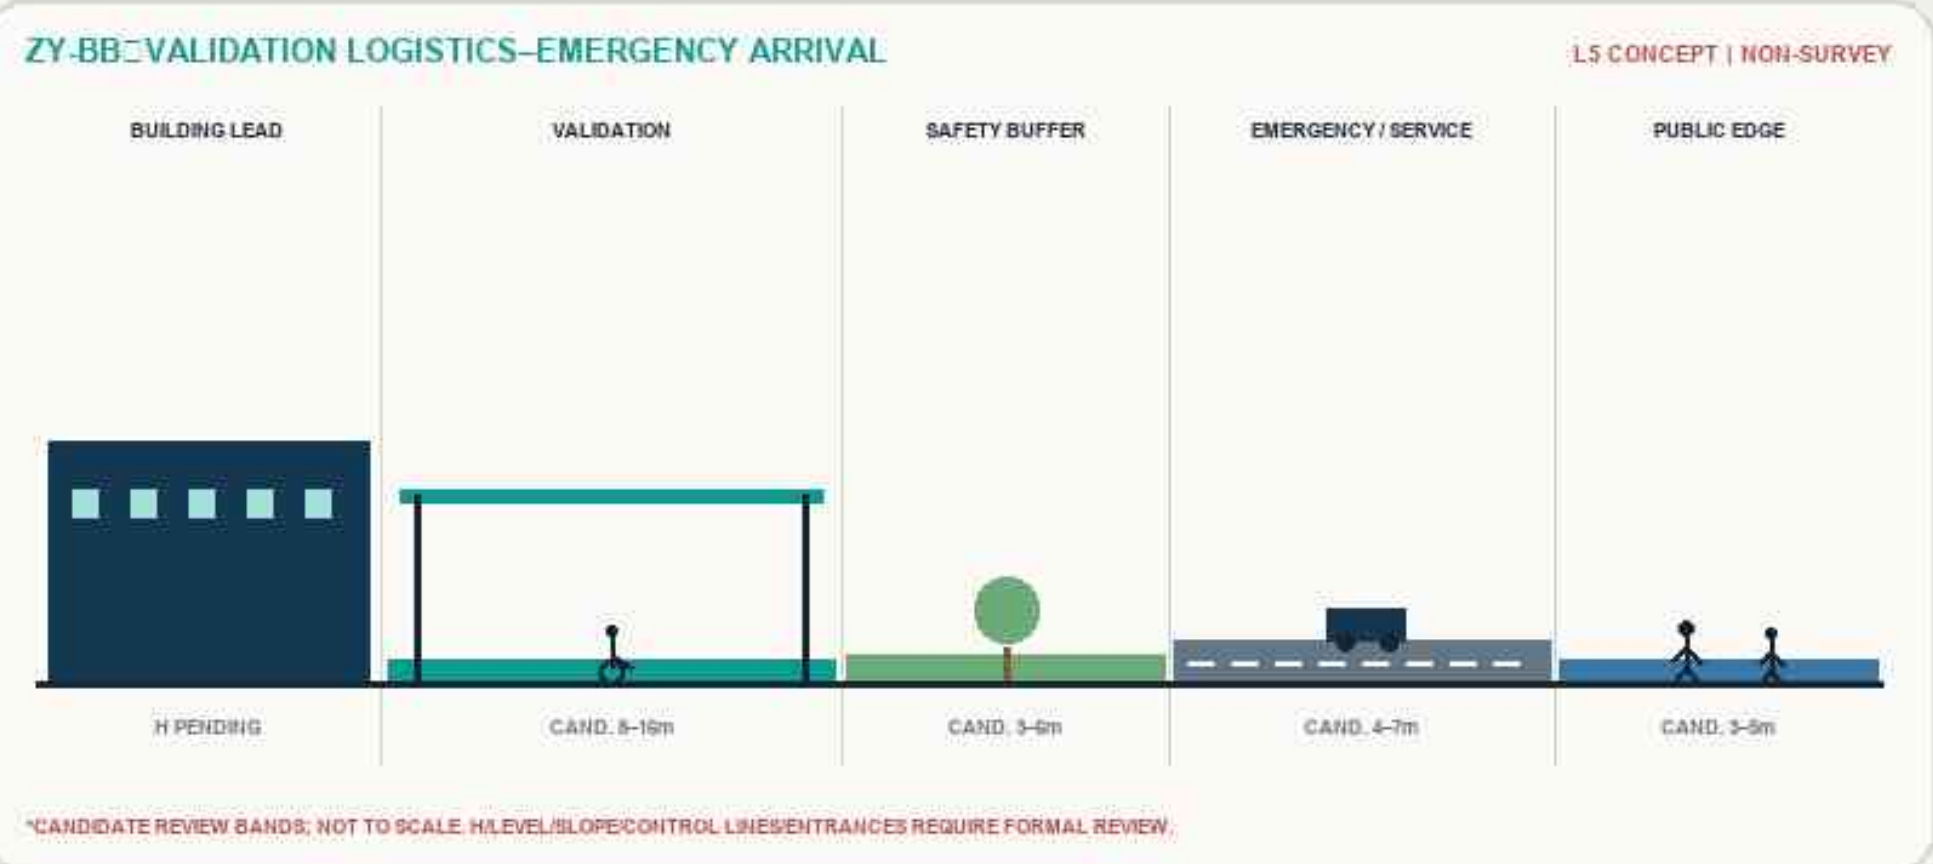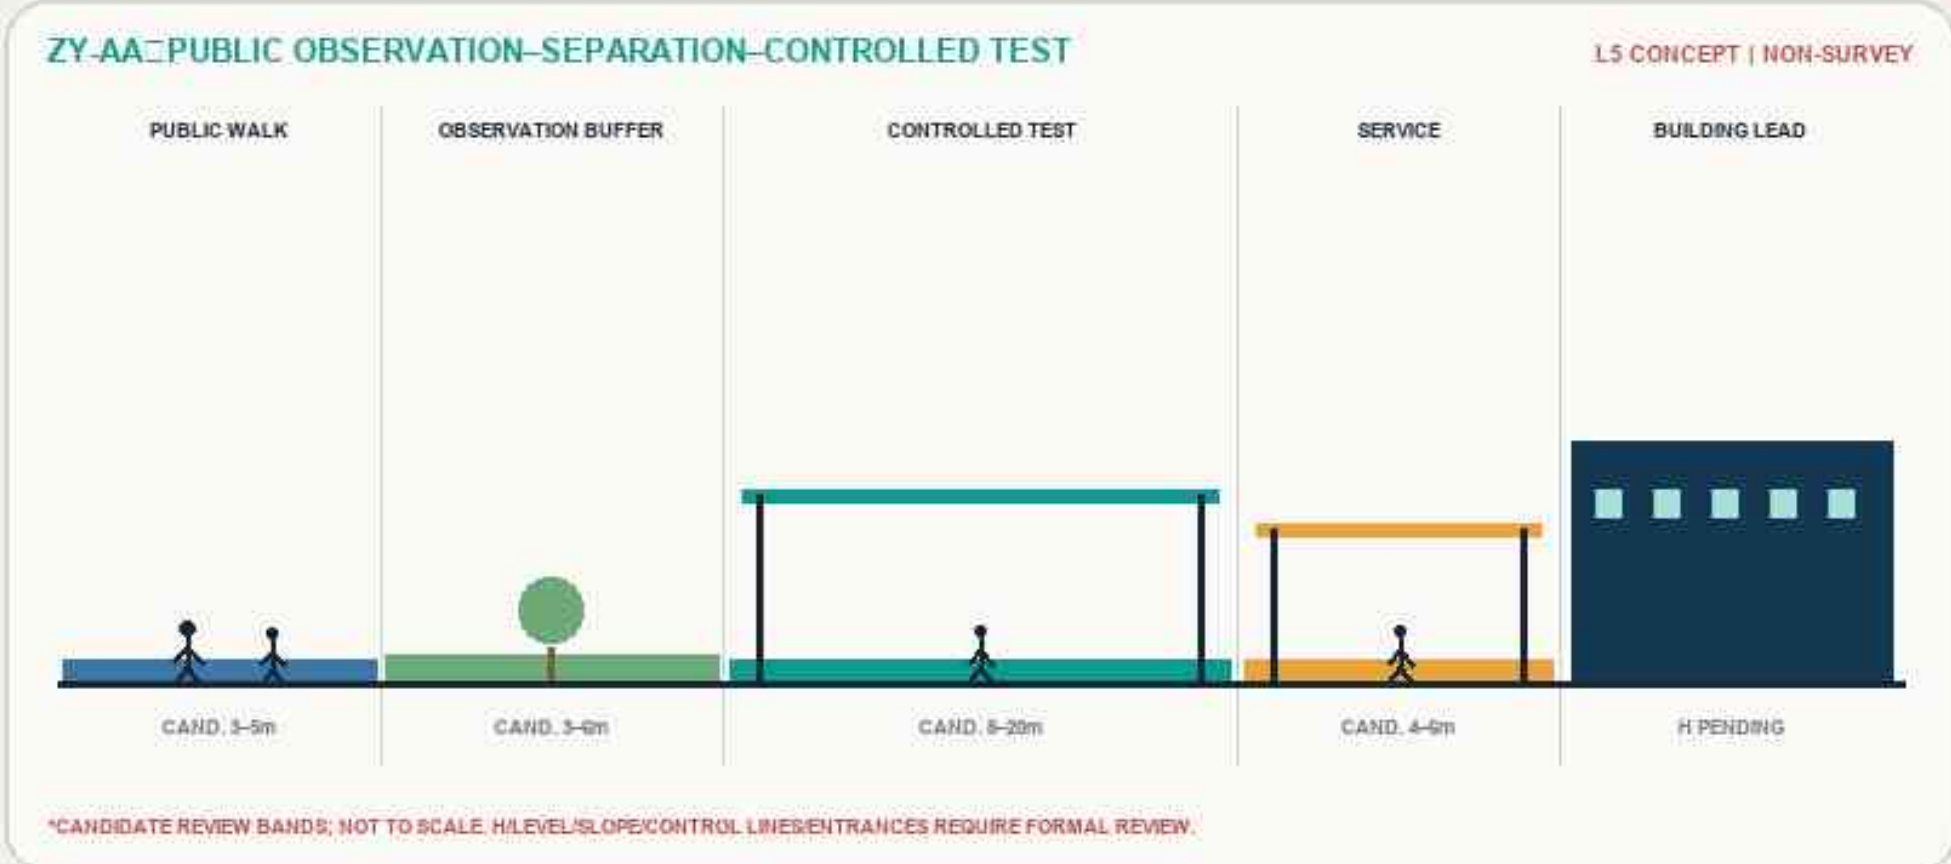

C2 / KEY-AREA PLAN-SECTION-OPERATION


AI Origin · Distributed Demand-Coordination Network

Prioritise the ground-floor hall at Origin Building, 8 Zhongguancun East Road, whose existing fit-out passed joint acceptance; RailWeave site authority, field baseline, and duty acceptance remain pending.

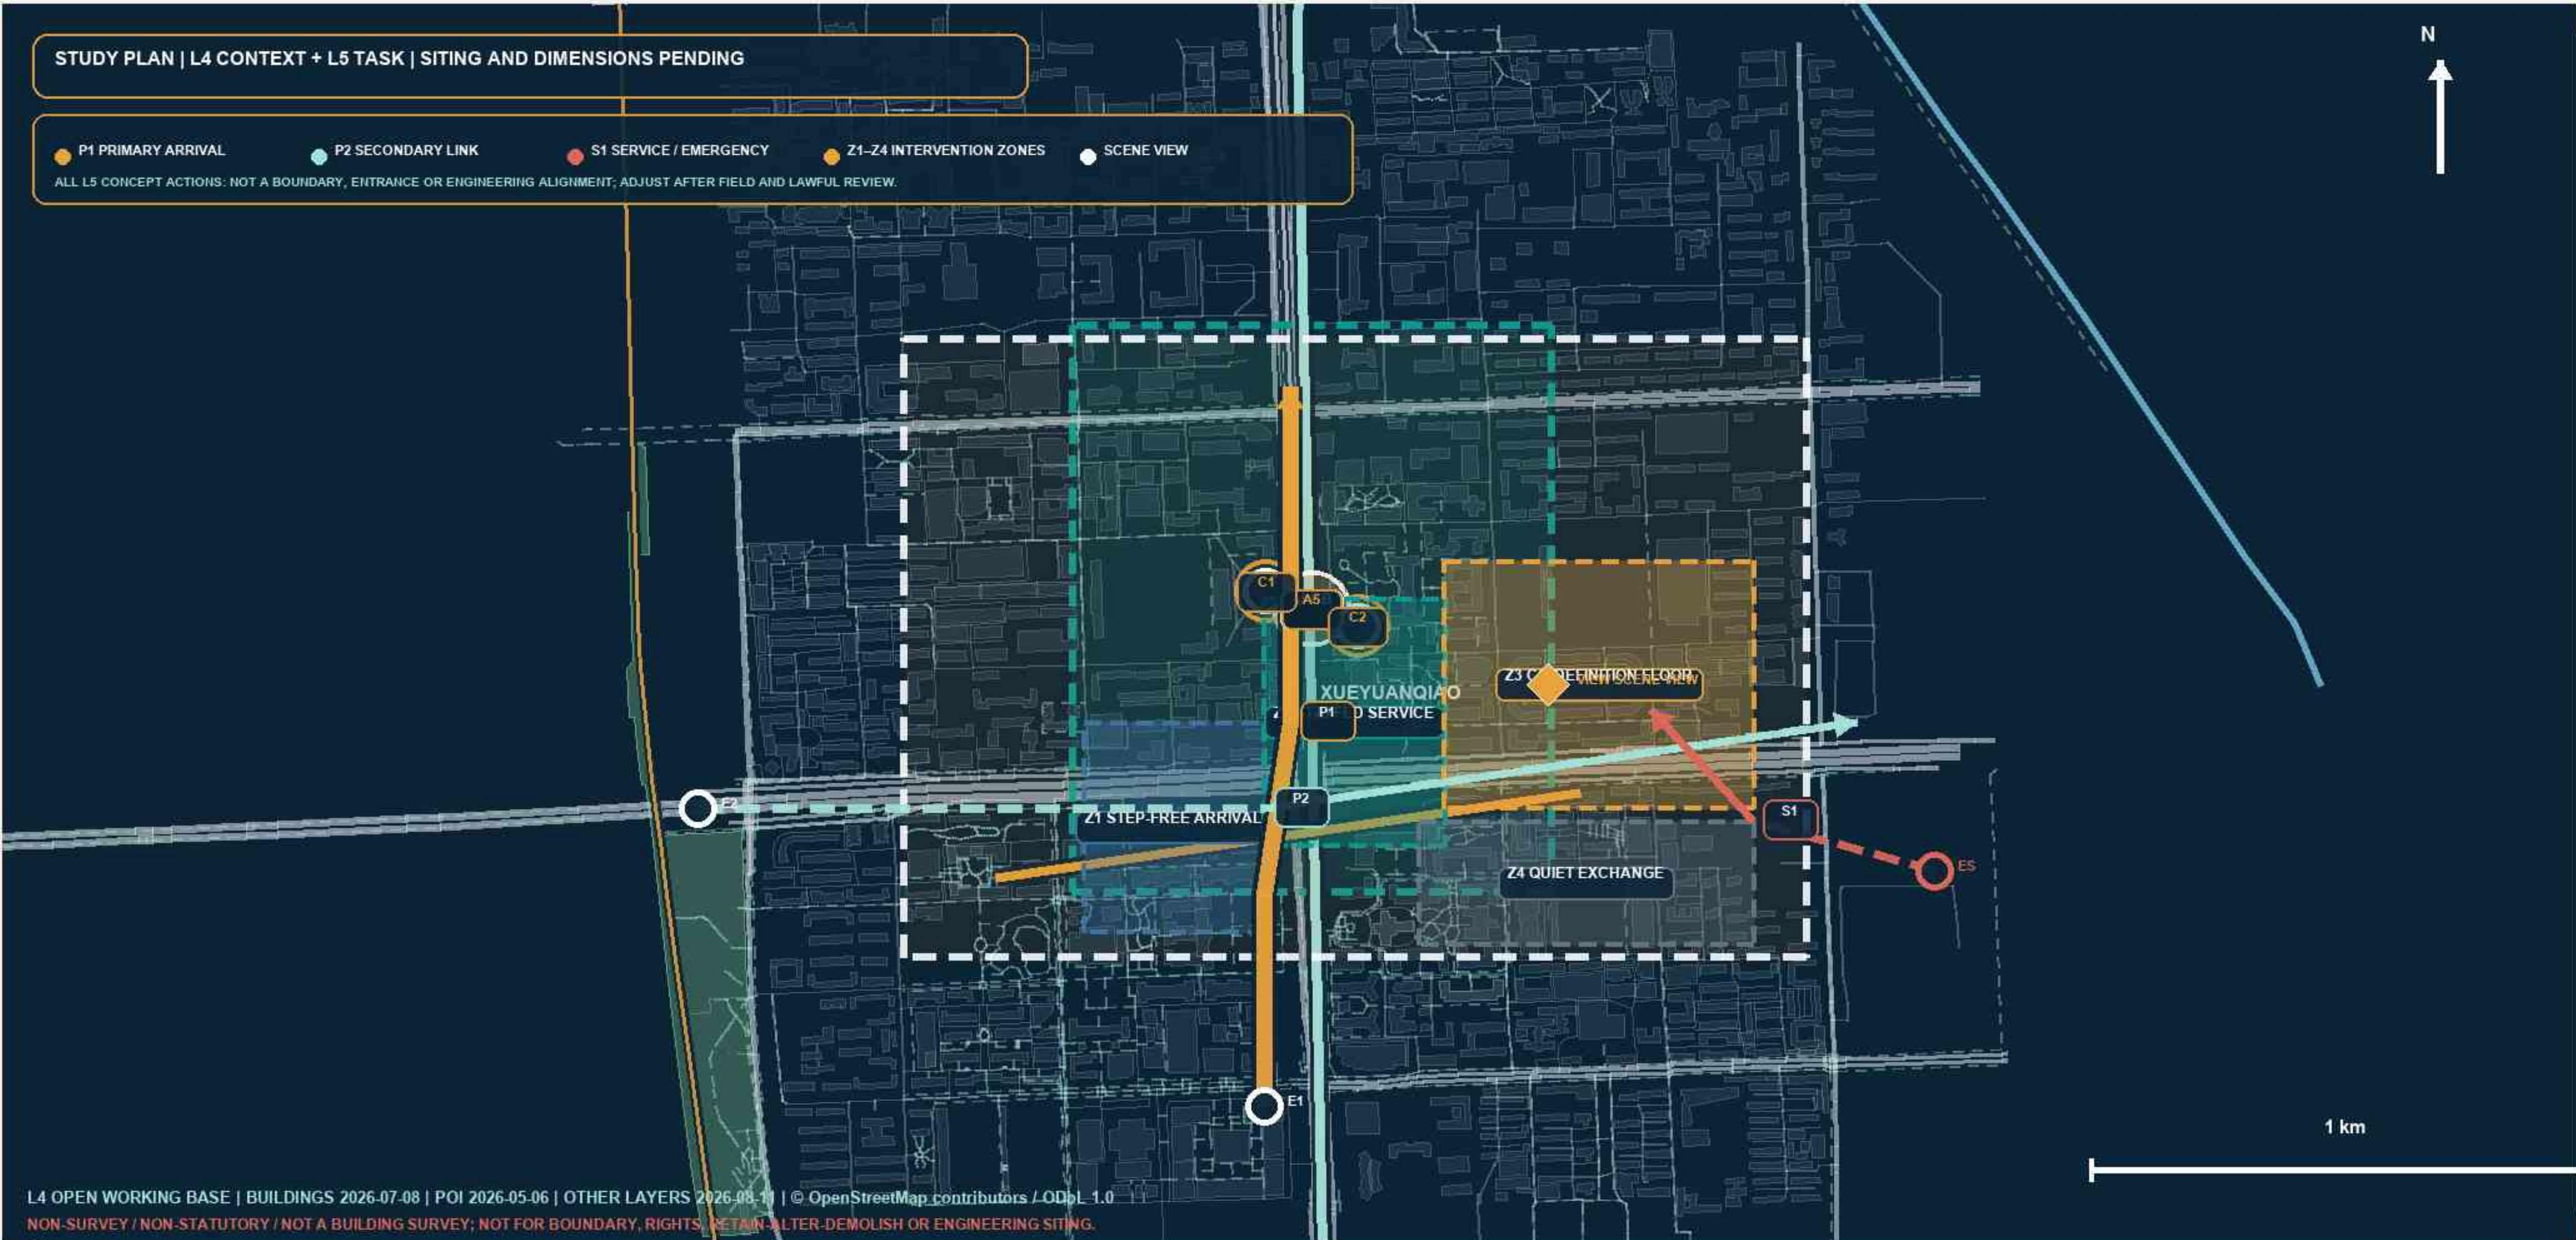

CANDIDATE VENUE AND REVIEW INTERFACES

PUBLIC ADDRESS	8 ZHONGGUANCUN EAST ROAD
EXISTING WORK	1,650 m² / 110108202606050403
ACCEPTANCE	2026-07-20 / HAI NO. 1380
DRAWING OBJECTS	KEY-002 / AN-005
COMPONENT	DC-AI-001 / DC-AI-002
PROJECT PENDING	SITE CONSENT / FIELD BASELINE / DUTY RECEIPT / PROJECT QUOTES

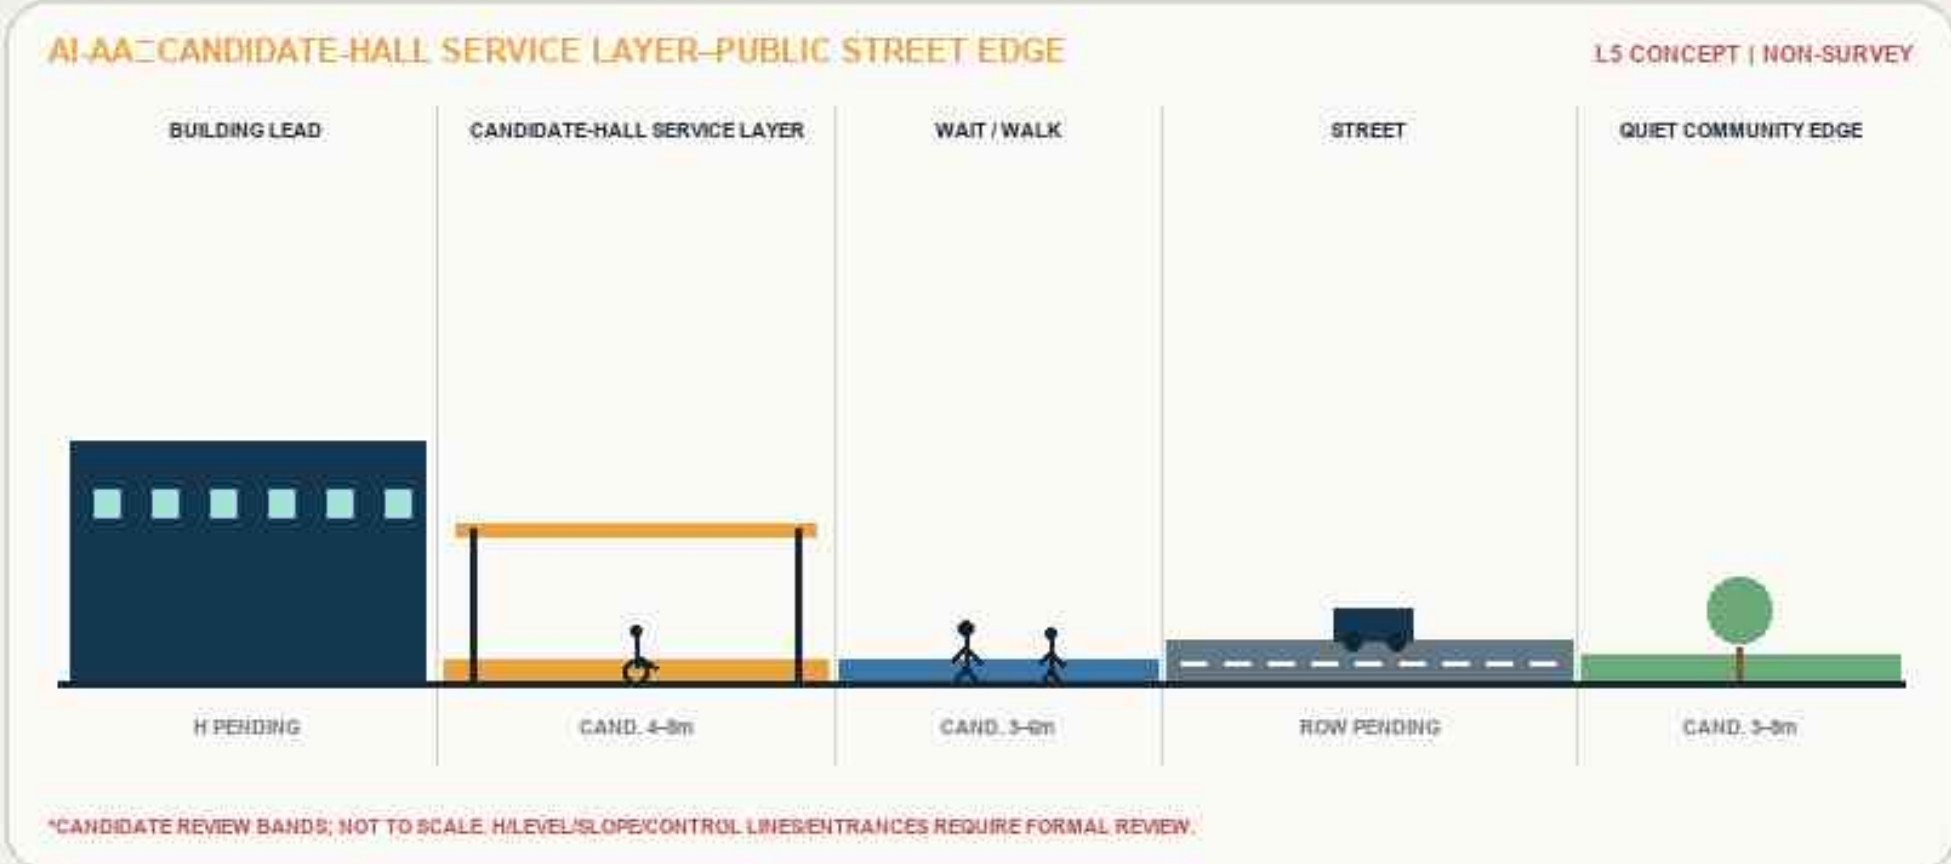

SPACE-OPERATION-EXIT LOOP




G0-G6 retains an audit trail; keep BLOCK if any site, rights, public, risk, cost, procurement or exit condition remains open.

C3 / KEY-AREA PLAN-SECTION-OPERATION




Dazhongsi · Station–City First-Use Interface

Organise surface continuity from the named Dazhongsi station's exterior context to demand service, the Jing-Zhang axis and Zhuan River; no specific entrance or underground connection is assumed.

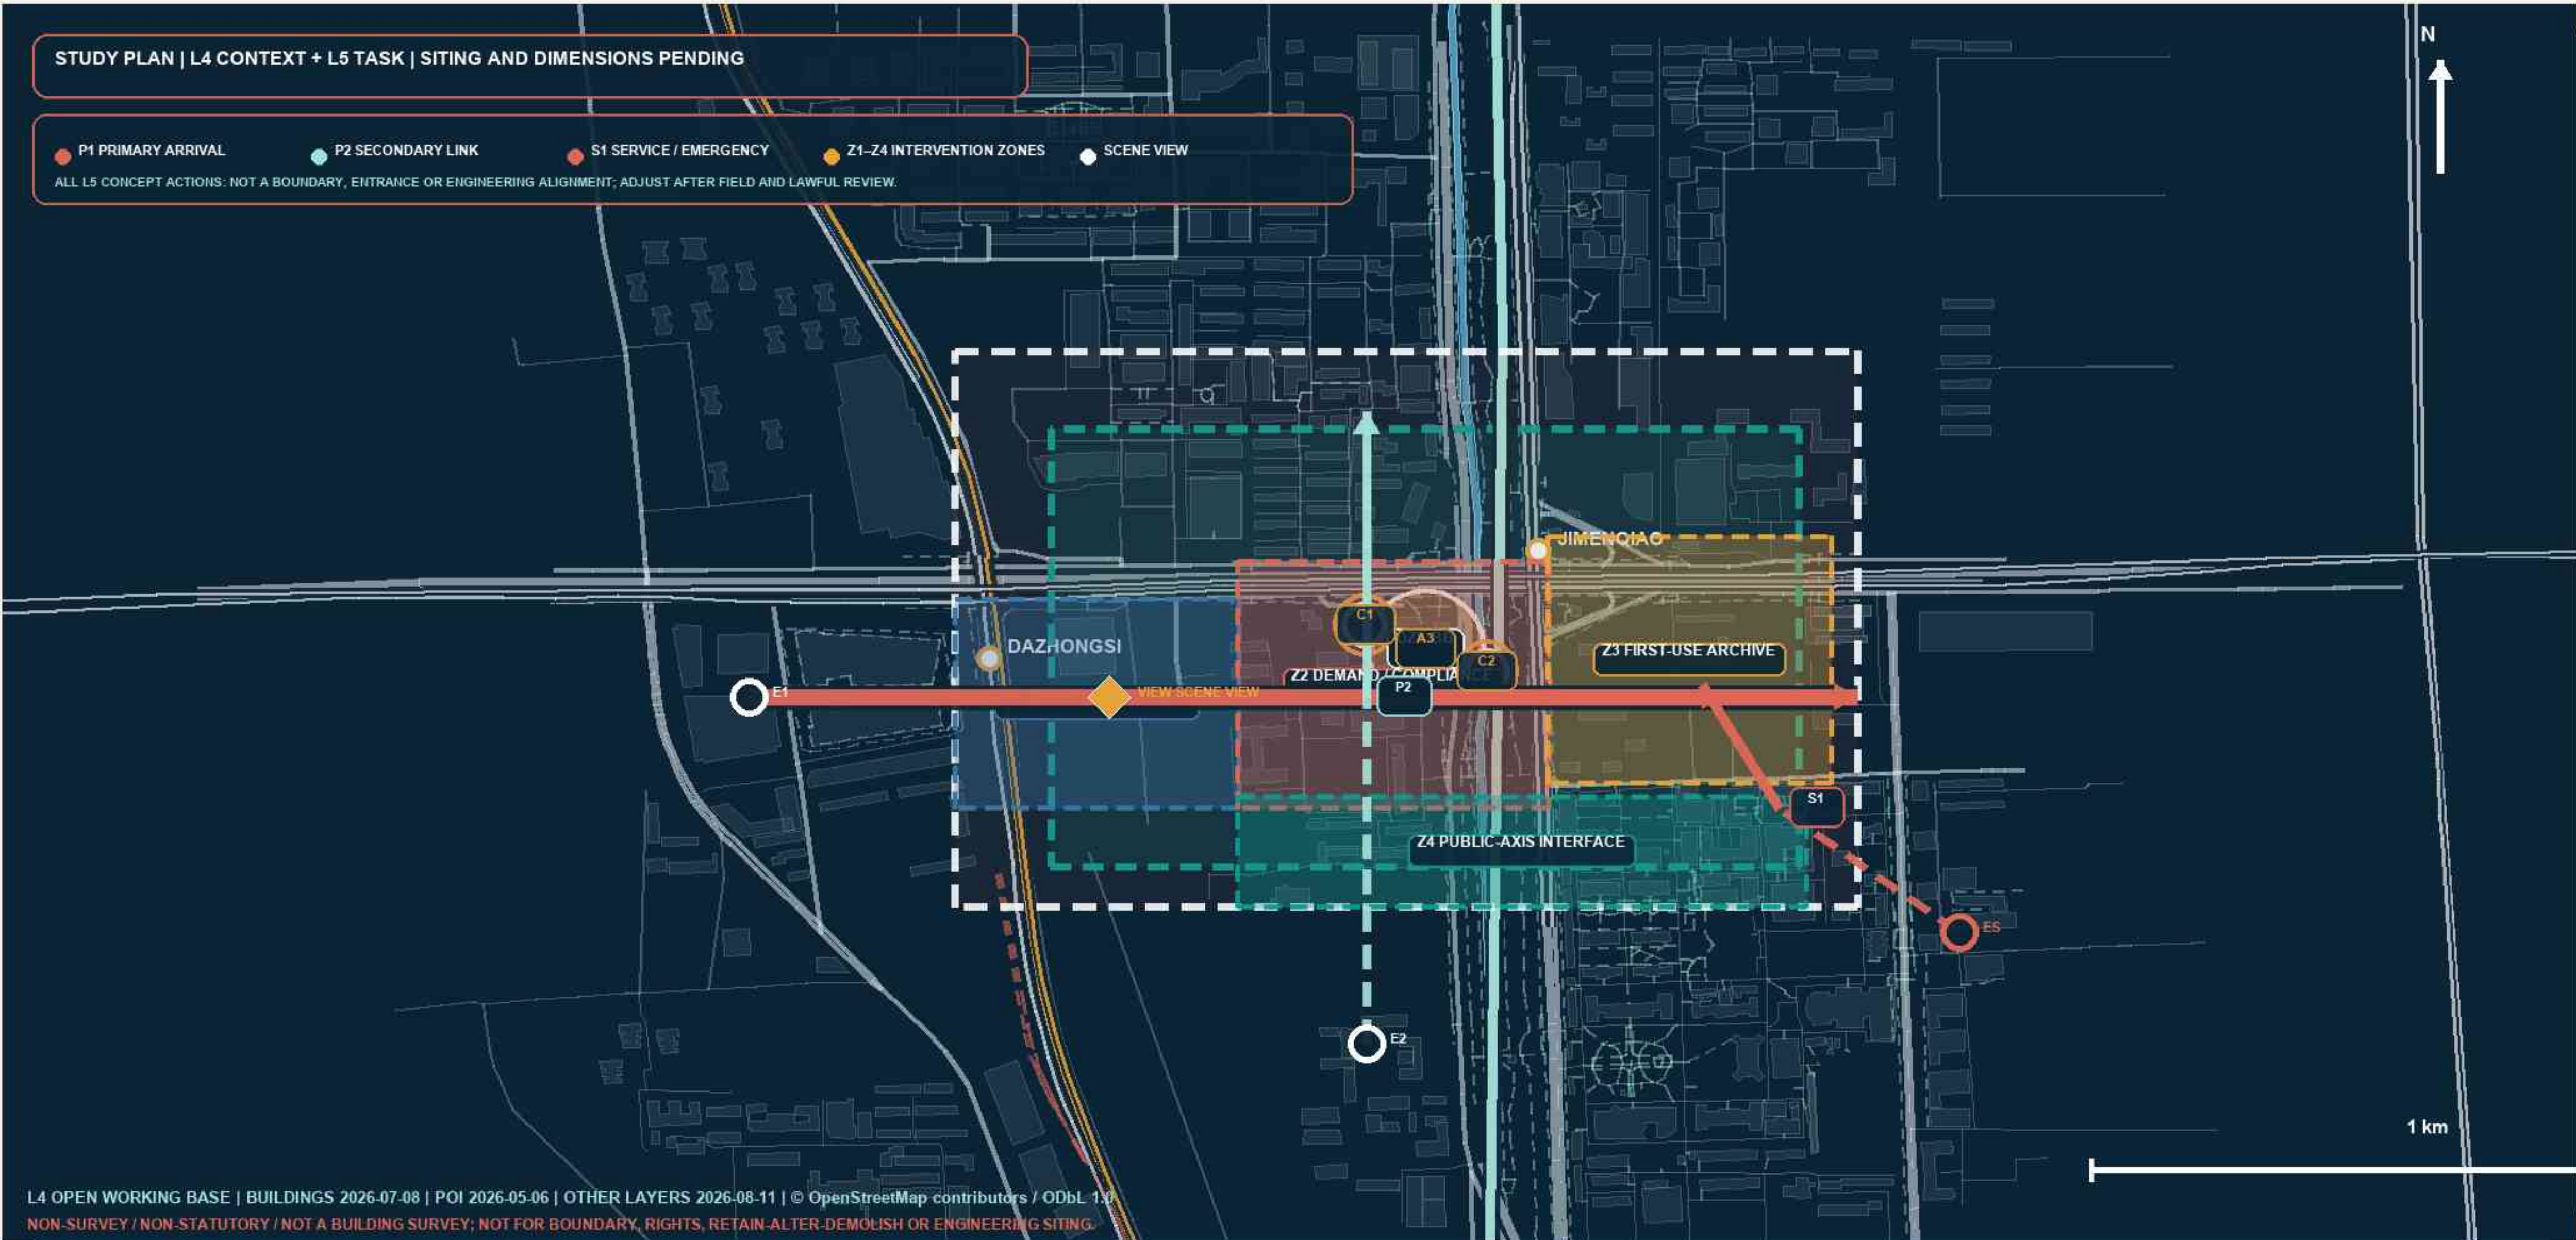

MAPPED OBJECTS AND REVIEW INTERFACES




WINDOW	KEY-003
AUDIT	AN-003
SECTION	SEC-DZS-AA / SEC-DZS-BB
COMPONENT	DC-DZS-001 / DC-DZS-002
PLAN ACTIONS	E1/E2/ES + P1/P2/S1 + Z1-Z4 + VIEW

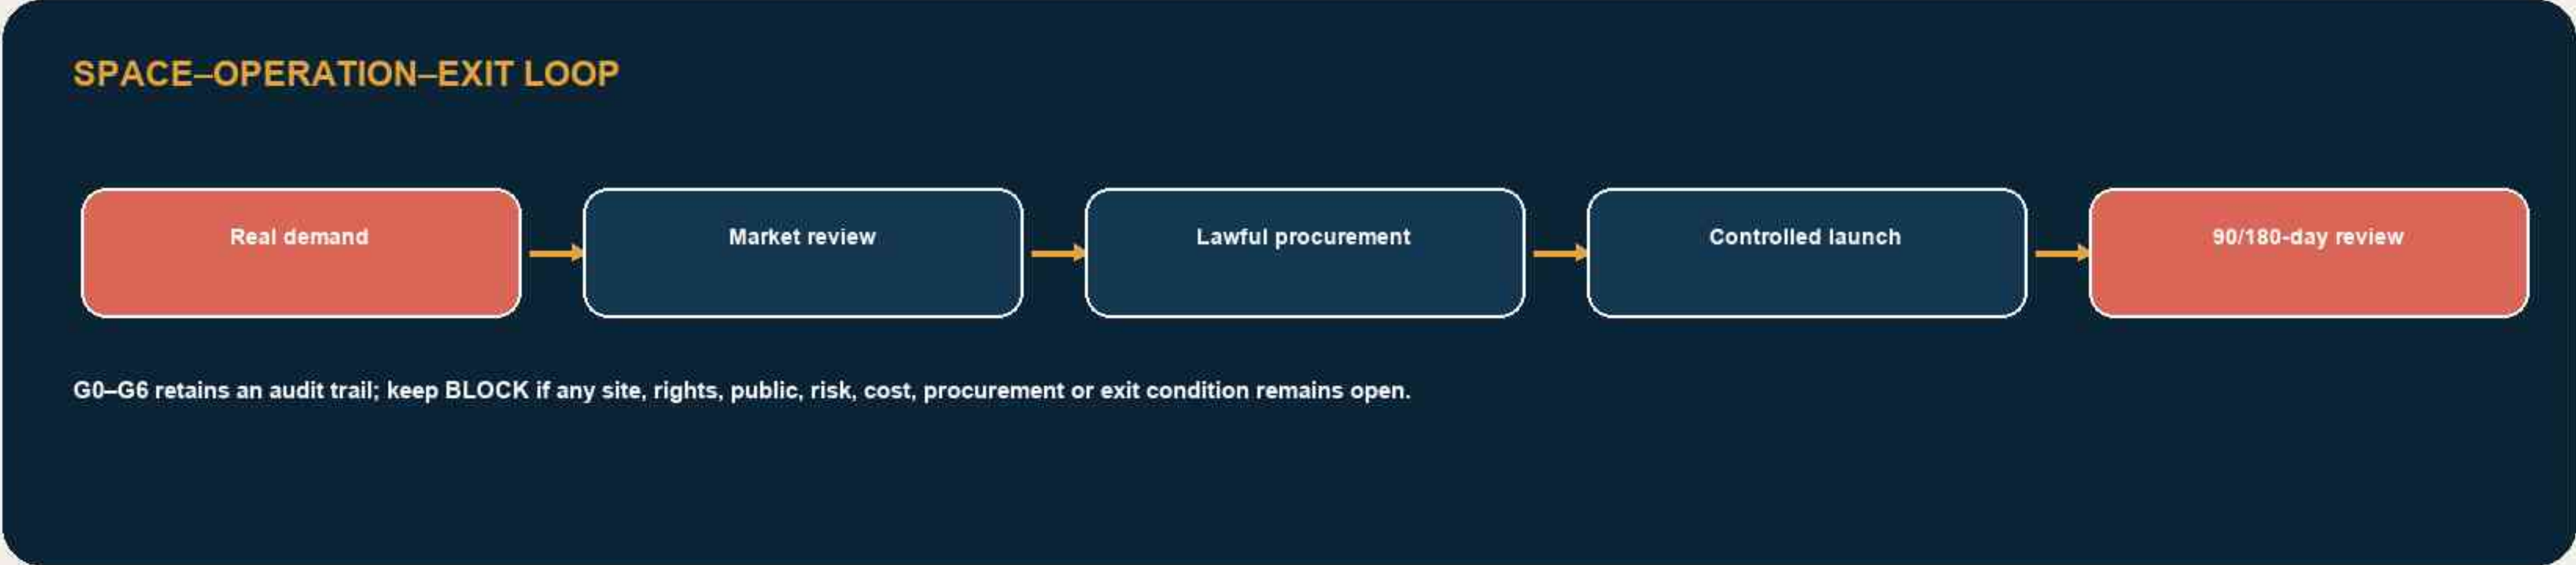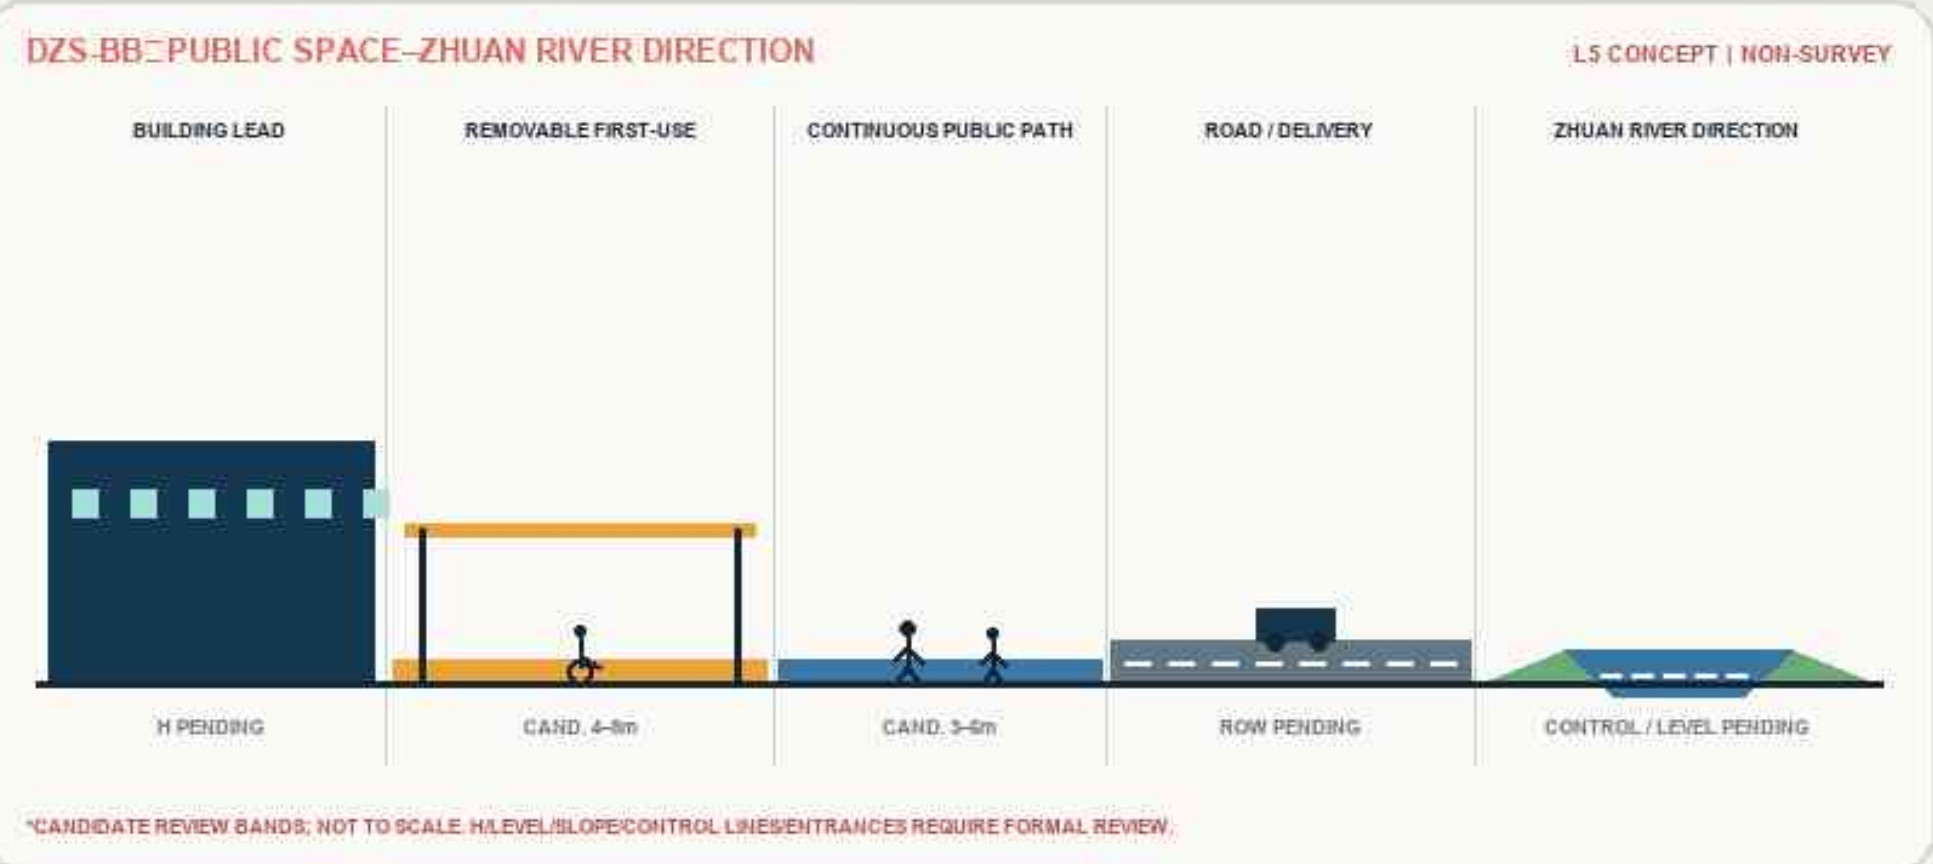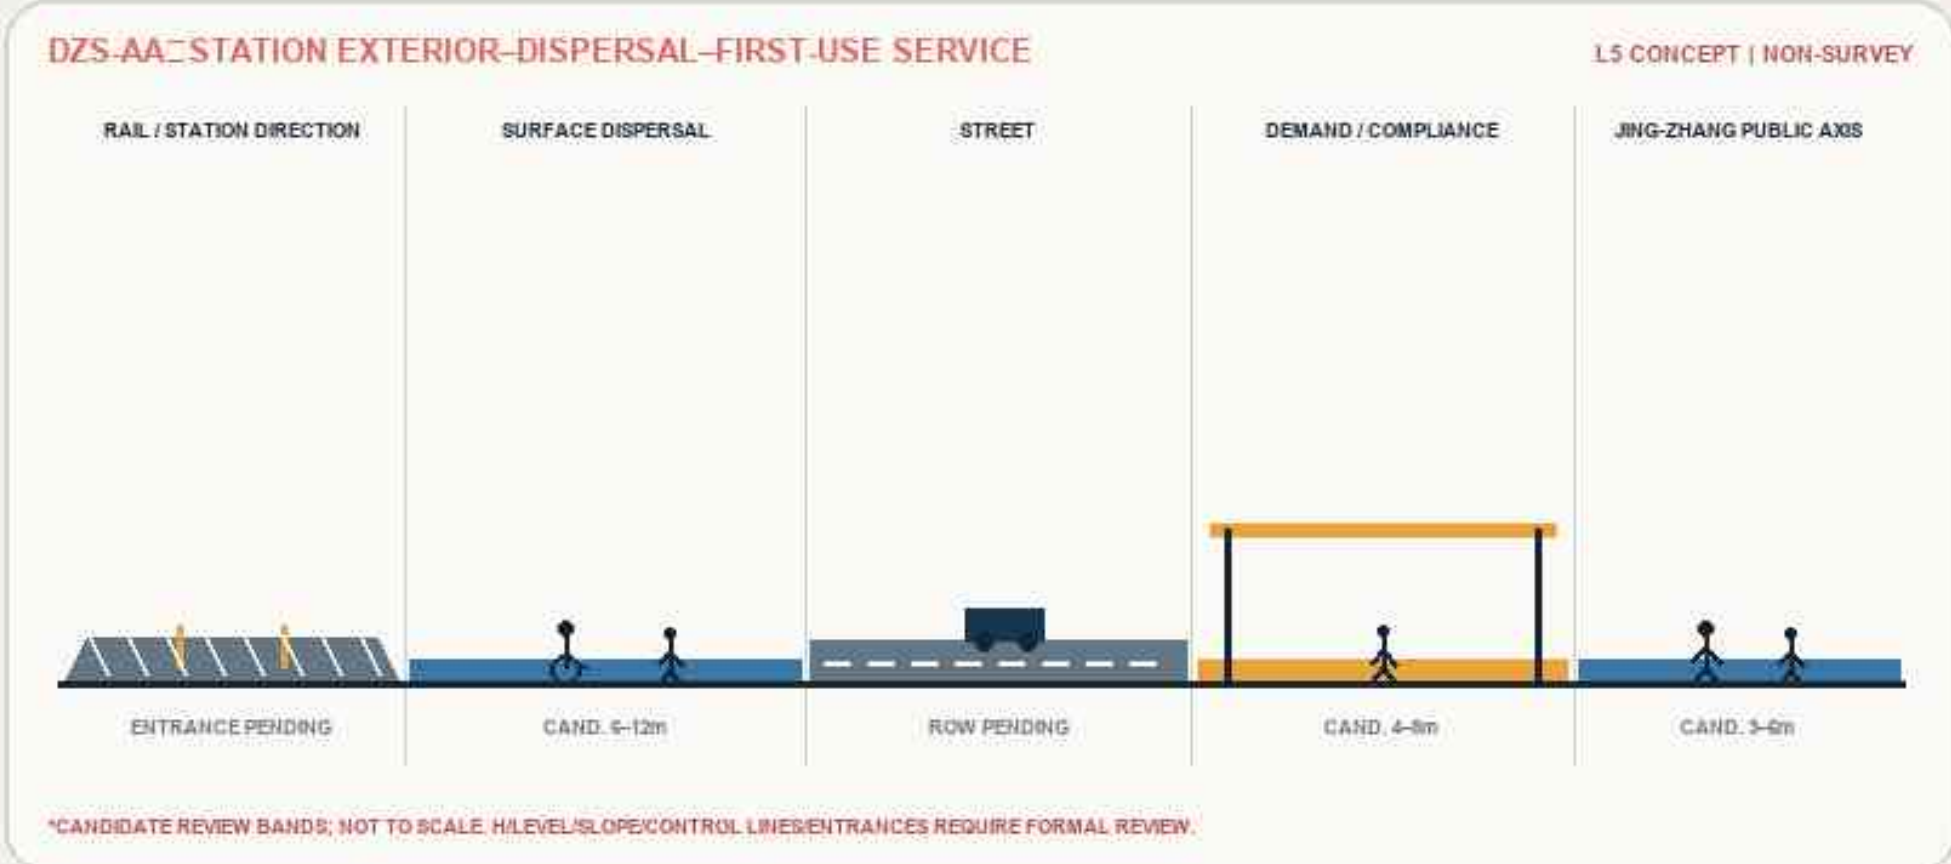

S01 / SIX CUT-LINES AND VARIABLE INTERFACES

Three Key Areas: Plan Location and Site-Concept Sections for Six Cut-Lines

AA/BB alignments are L5 study indexes; candidate width reviews, human scale and interface relationships do not establish surveyed conditions, statutory control lines, building heights, levels, entrances or engineering dimensions.

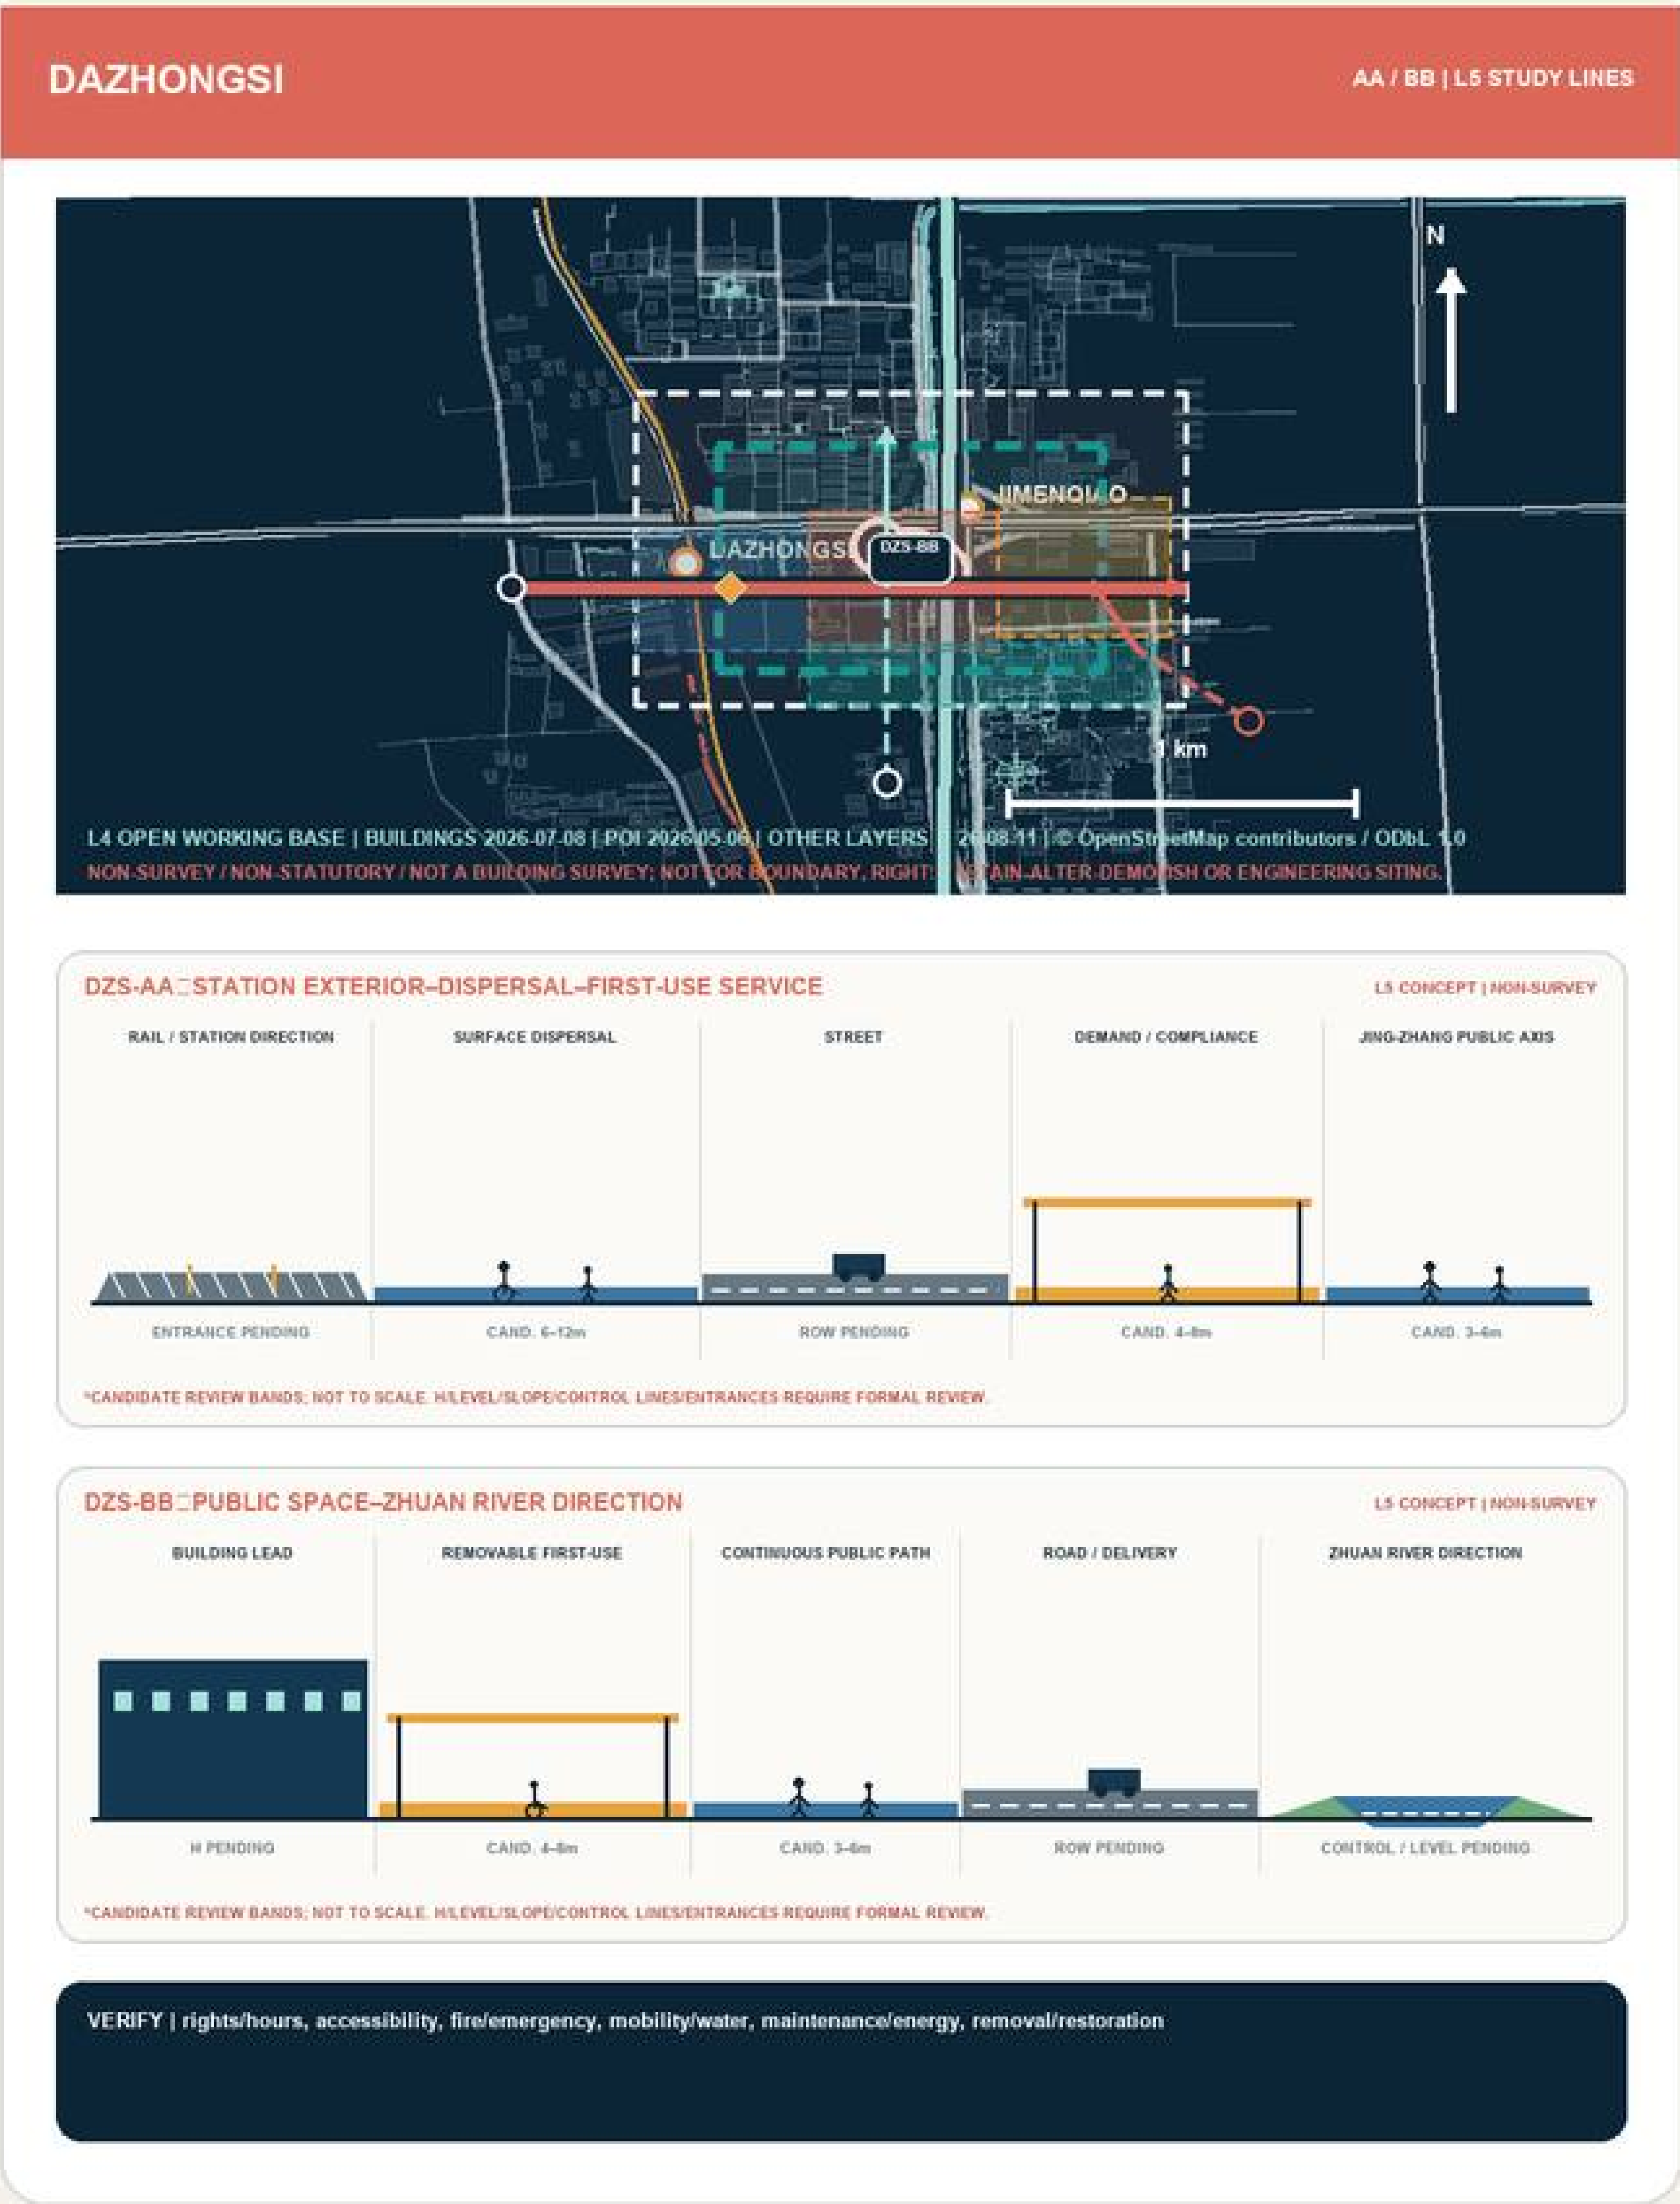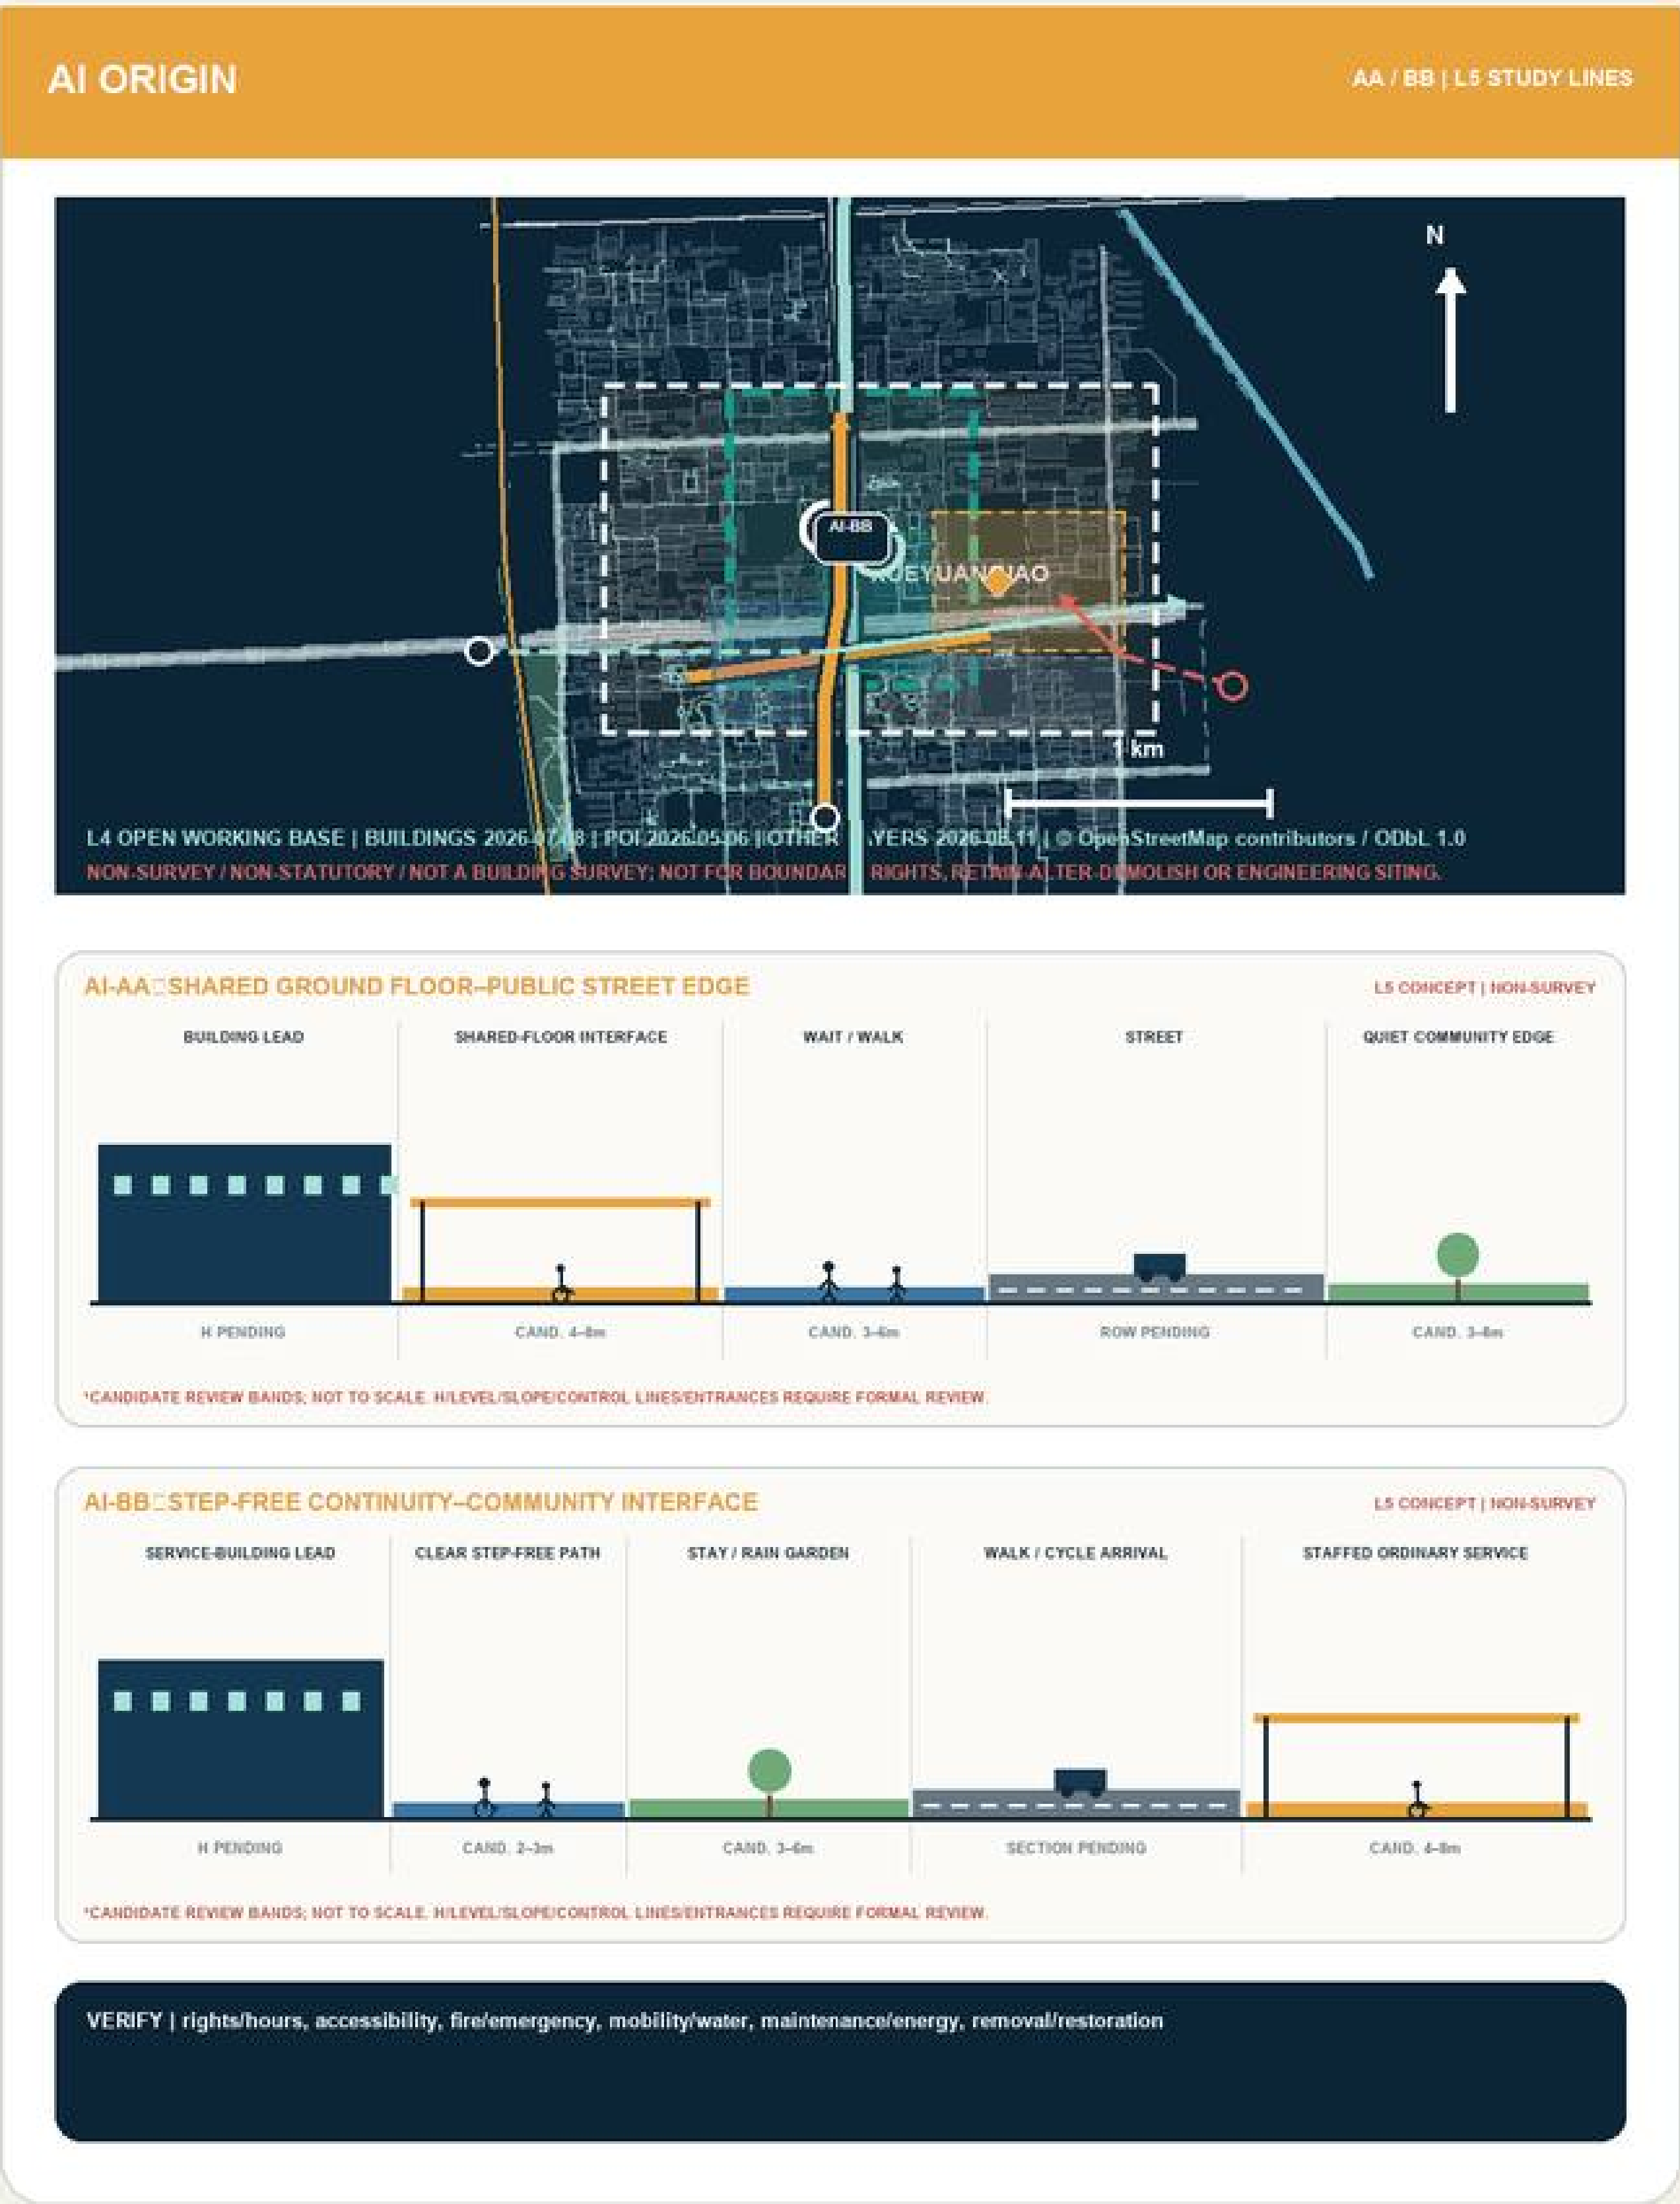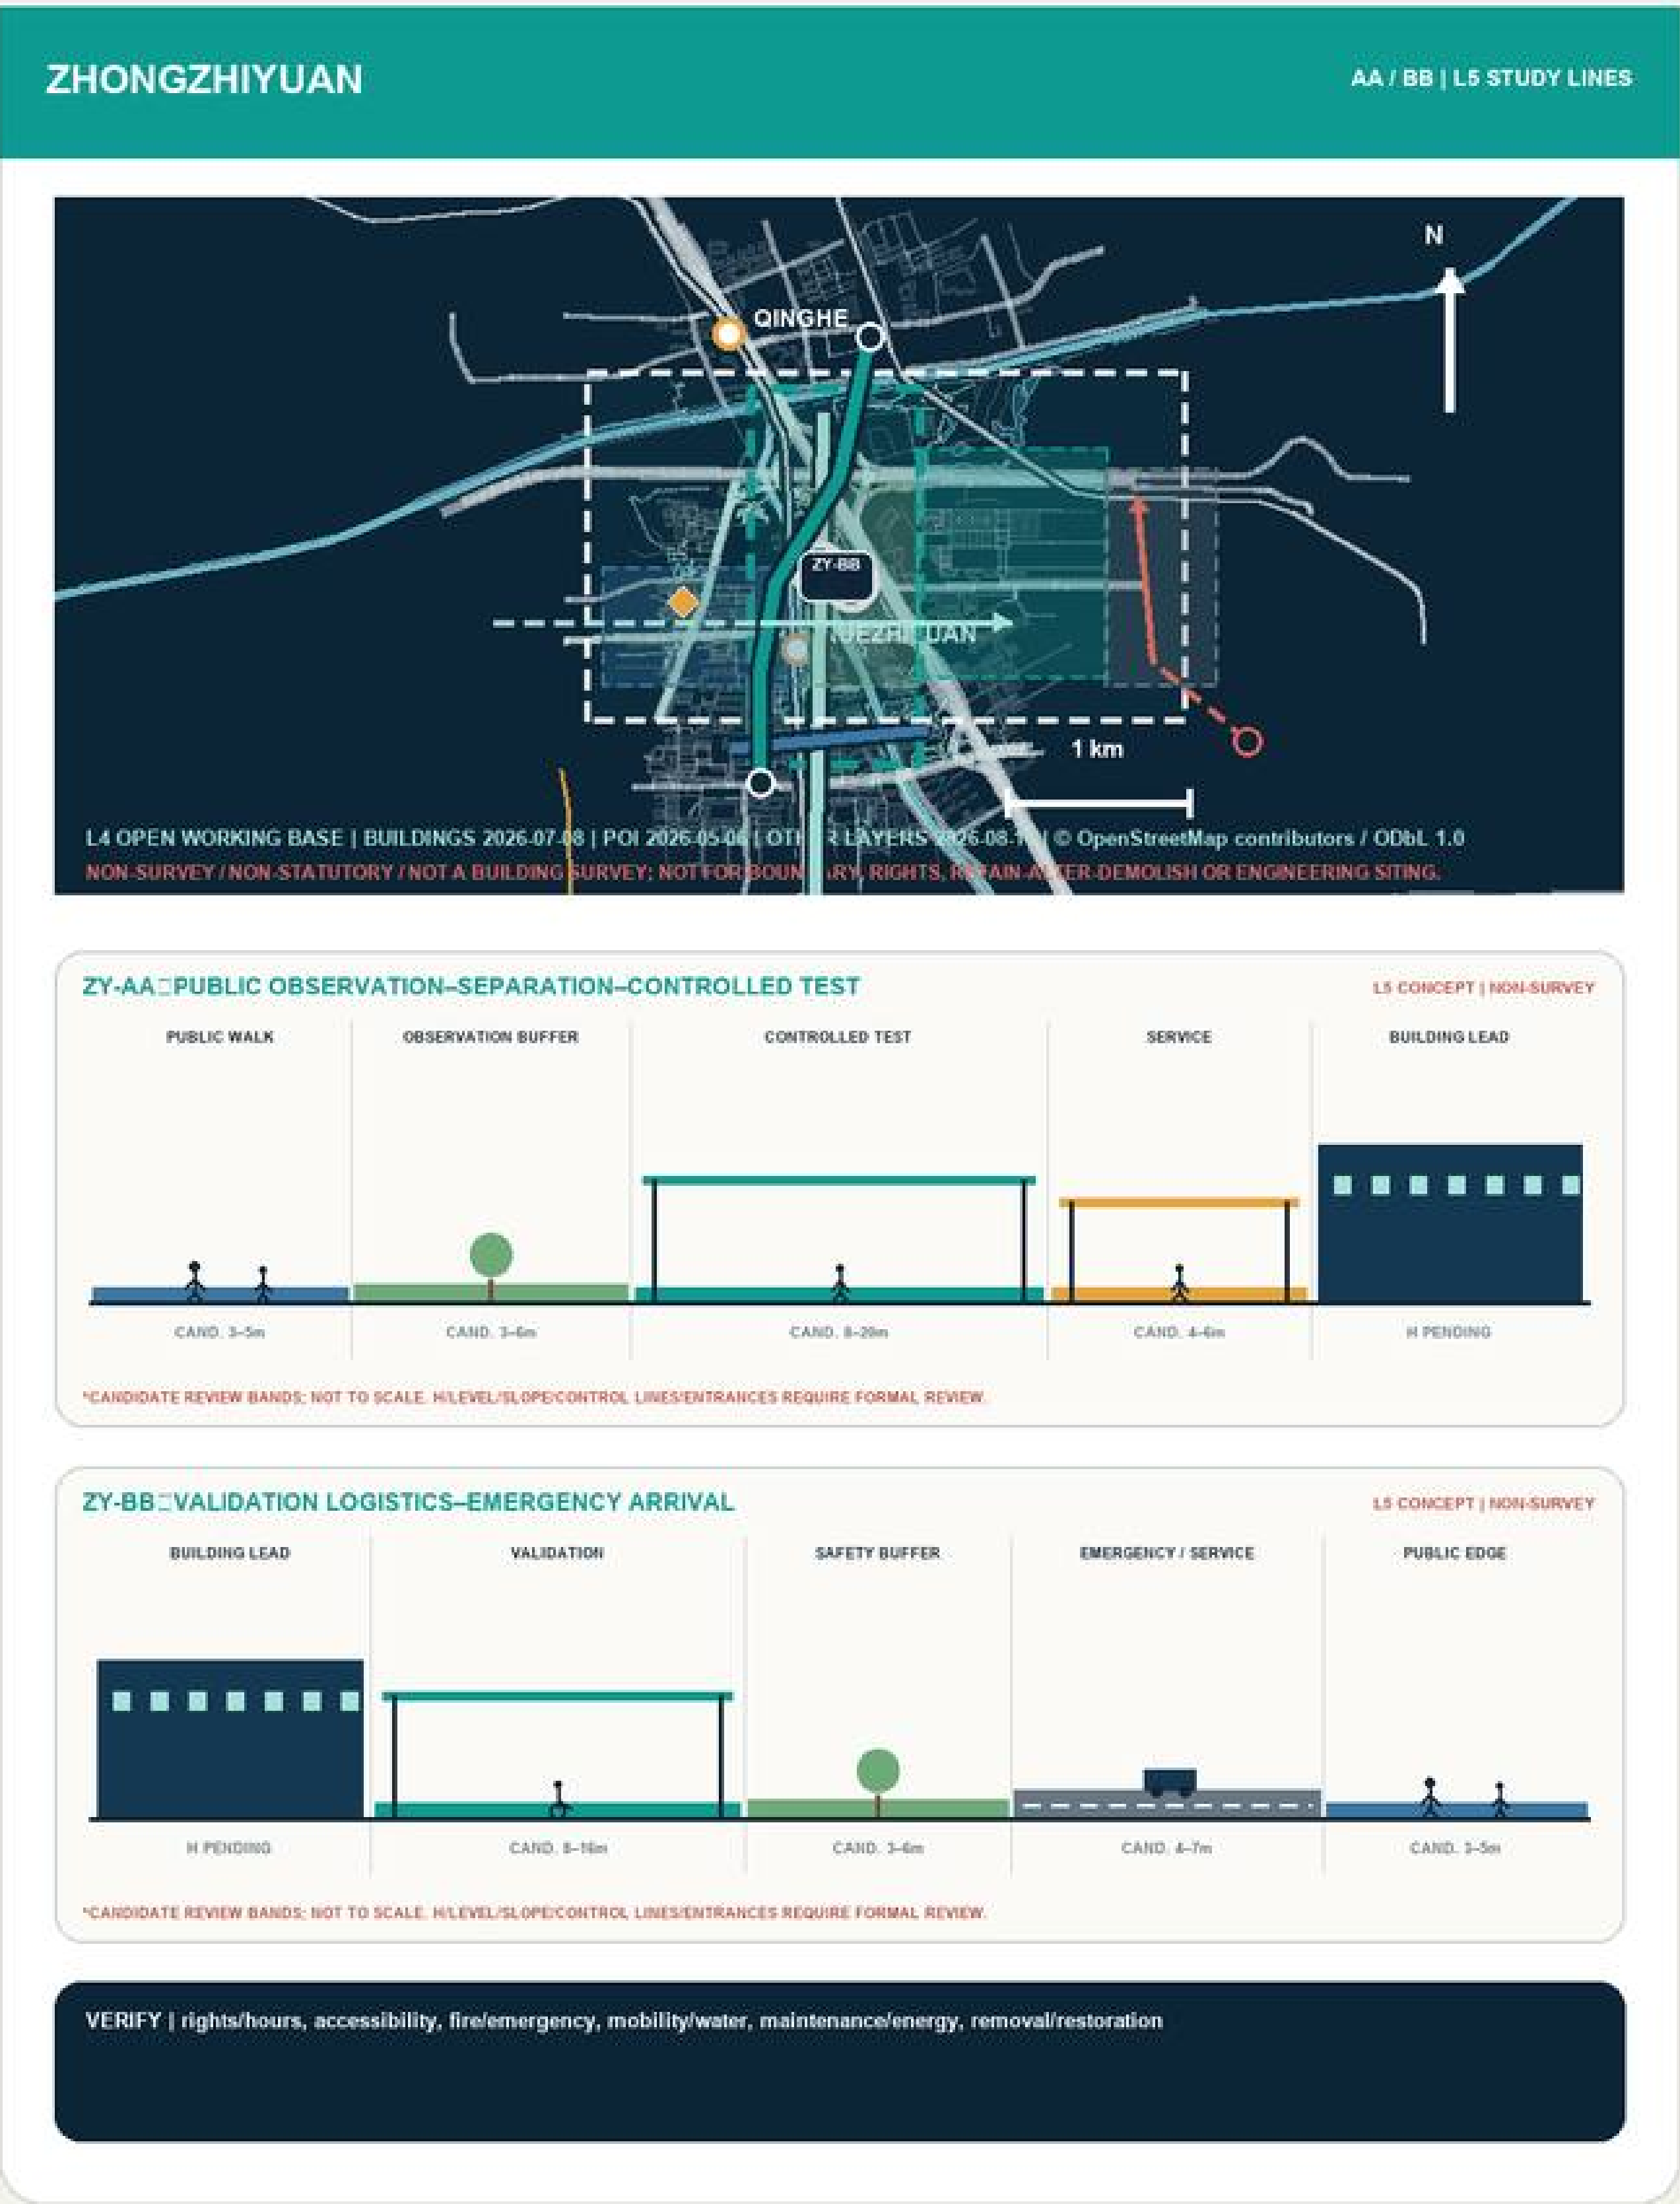

E01 / FOUR VERIFIABLE LOOPS

Spatial–AI–Delivery–Public Value: Four Verifiable Loops

All values count package, contract and verification-task completeness; they are not field performance, statutory metrics, approval or secured funding.

01 SPATIAL EVIDENCE

1 + 3 + 3

axis / corridors / study windows

9 + 8

field-audit segments / anchors

6 + 6

variable sections / reversible components

L5 provisional geometry; official boundary, rights and baseline remain pending.

02 AI GOVERNANCE

12 / 12

dual independent-gate coverage

12 / 12

human final-review coverage

72 / 1,498

synthetic branches / passed assertions

All 60 defect branches fail closed; synthetic PASS does not prove real-world efficacy.

03 DELIVERY HANDOFF

3

whole-life project registers

G0–G6

seven gates: evidence to exit

8 + 10

handoff checks / cost-evidence items

Role placeholder–lawful appointment–written receipt; unverified prices stay outside totals.

04 PUBLIC VALUE

12 / 12

ordinary-service equivalence

12 / 12

exit-restoration receipt coverage

90 / 180

post-deployment review points

Refusing AI adds no charge, unreasonable wait or off-site trip; appeals go to people.



SPATIAL SCALE (READ BY EVIDENCE LEVEL): official written study scale ≈11.4 km² | three key-area task scales total ≈368.4 ha | L4/L5 boundary diagnostic ≈413 m.

PENDING: official boundaries | FAR and height | building baseline and rights | continuously open length | quantities, prices, budget and accountable entities.

D00 / EVIDENCE & BOUNDARY

Evidence, Boundary and Design-Depth Control


Review confirmed facts, working basemap, provisional geometry and design proposals as separate evidence classes.

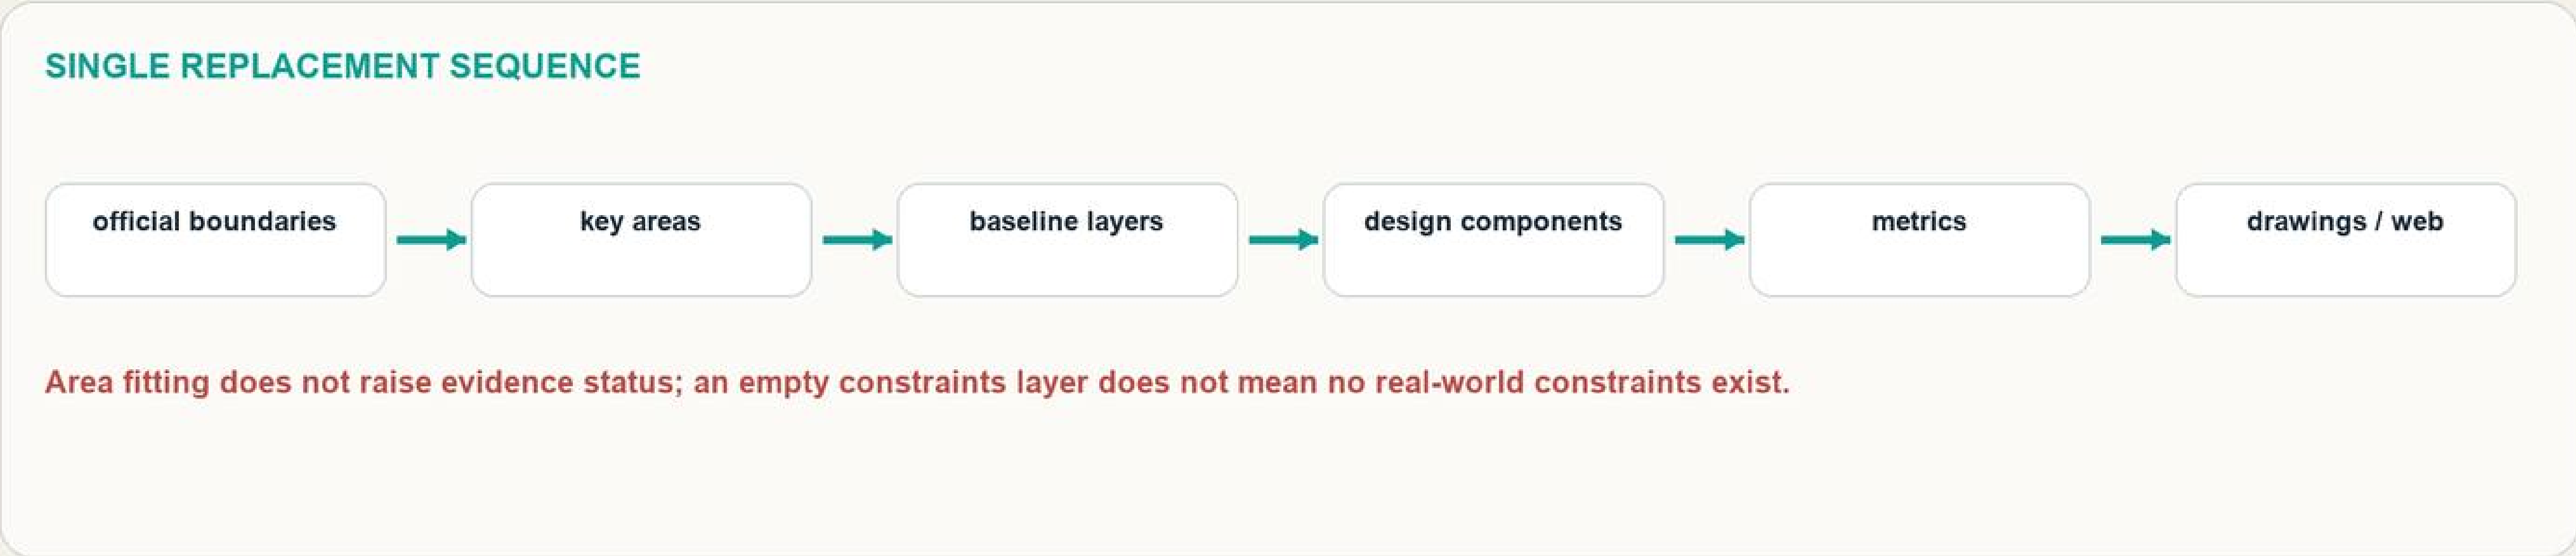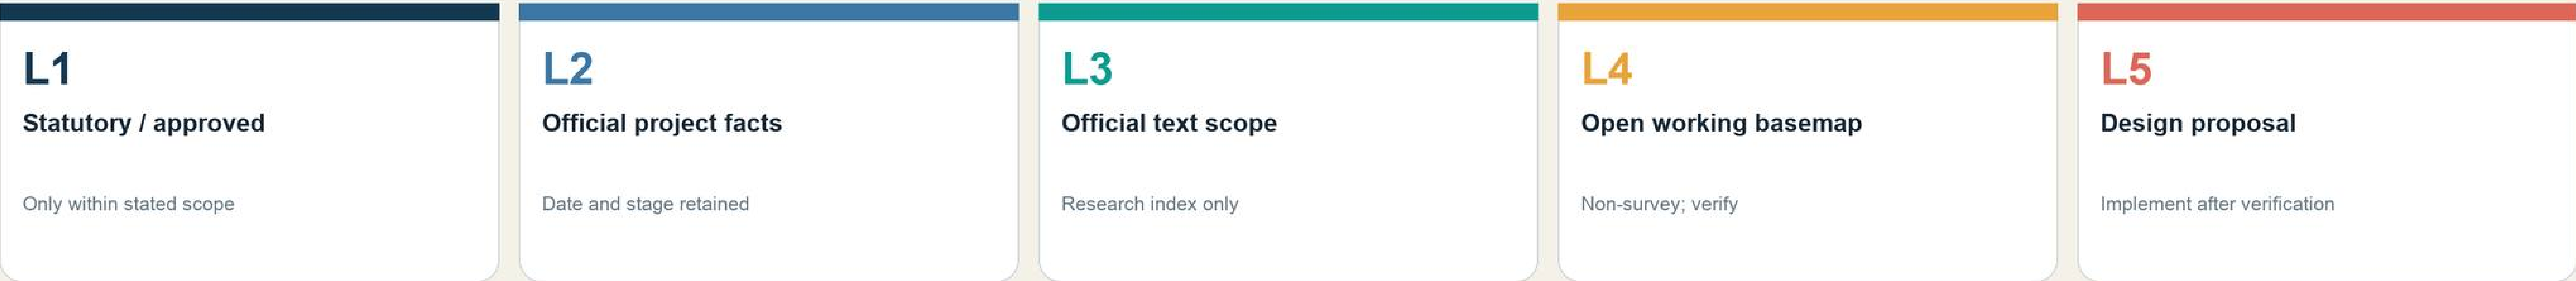

AI01 / SERVICE BLUEPRINTS


Three AI Concept Prototype Specifications

Each prototype delivers a service blueprint, spatial interface, data flow, responsibility matrix, and acceptance/stop criteria.

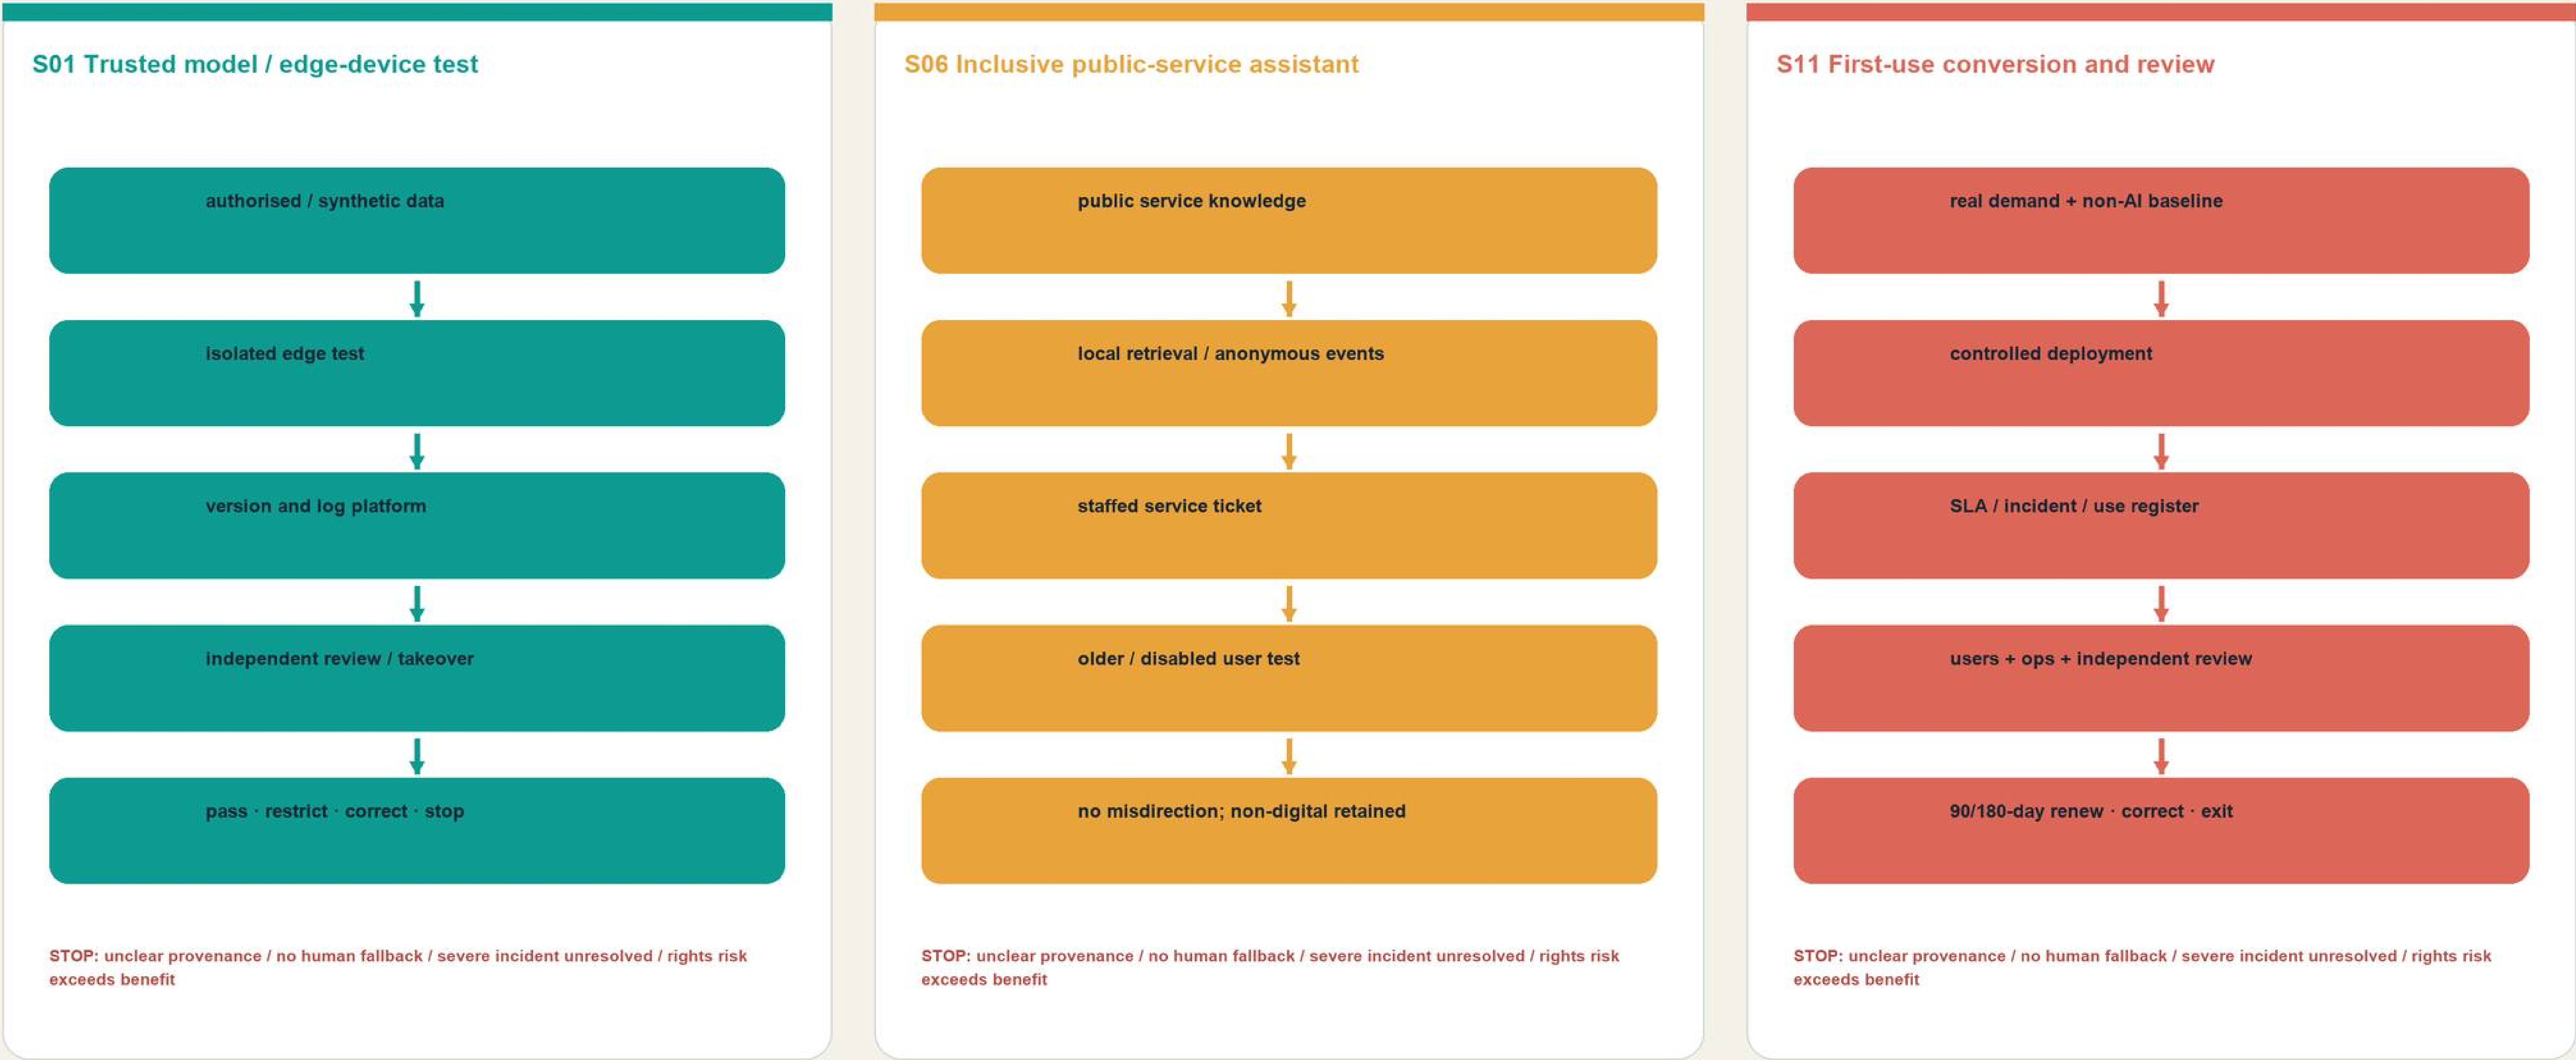

Public Participation, Public Value and Risk-Governance Loop

Public participation is embedded in demand formation, prototype observation, operating review and exit decisions.

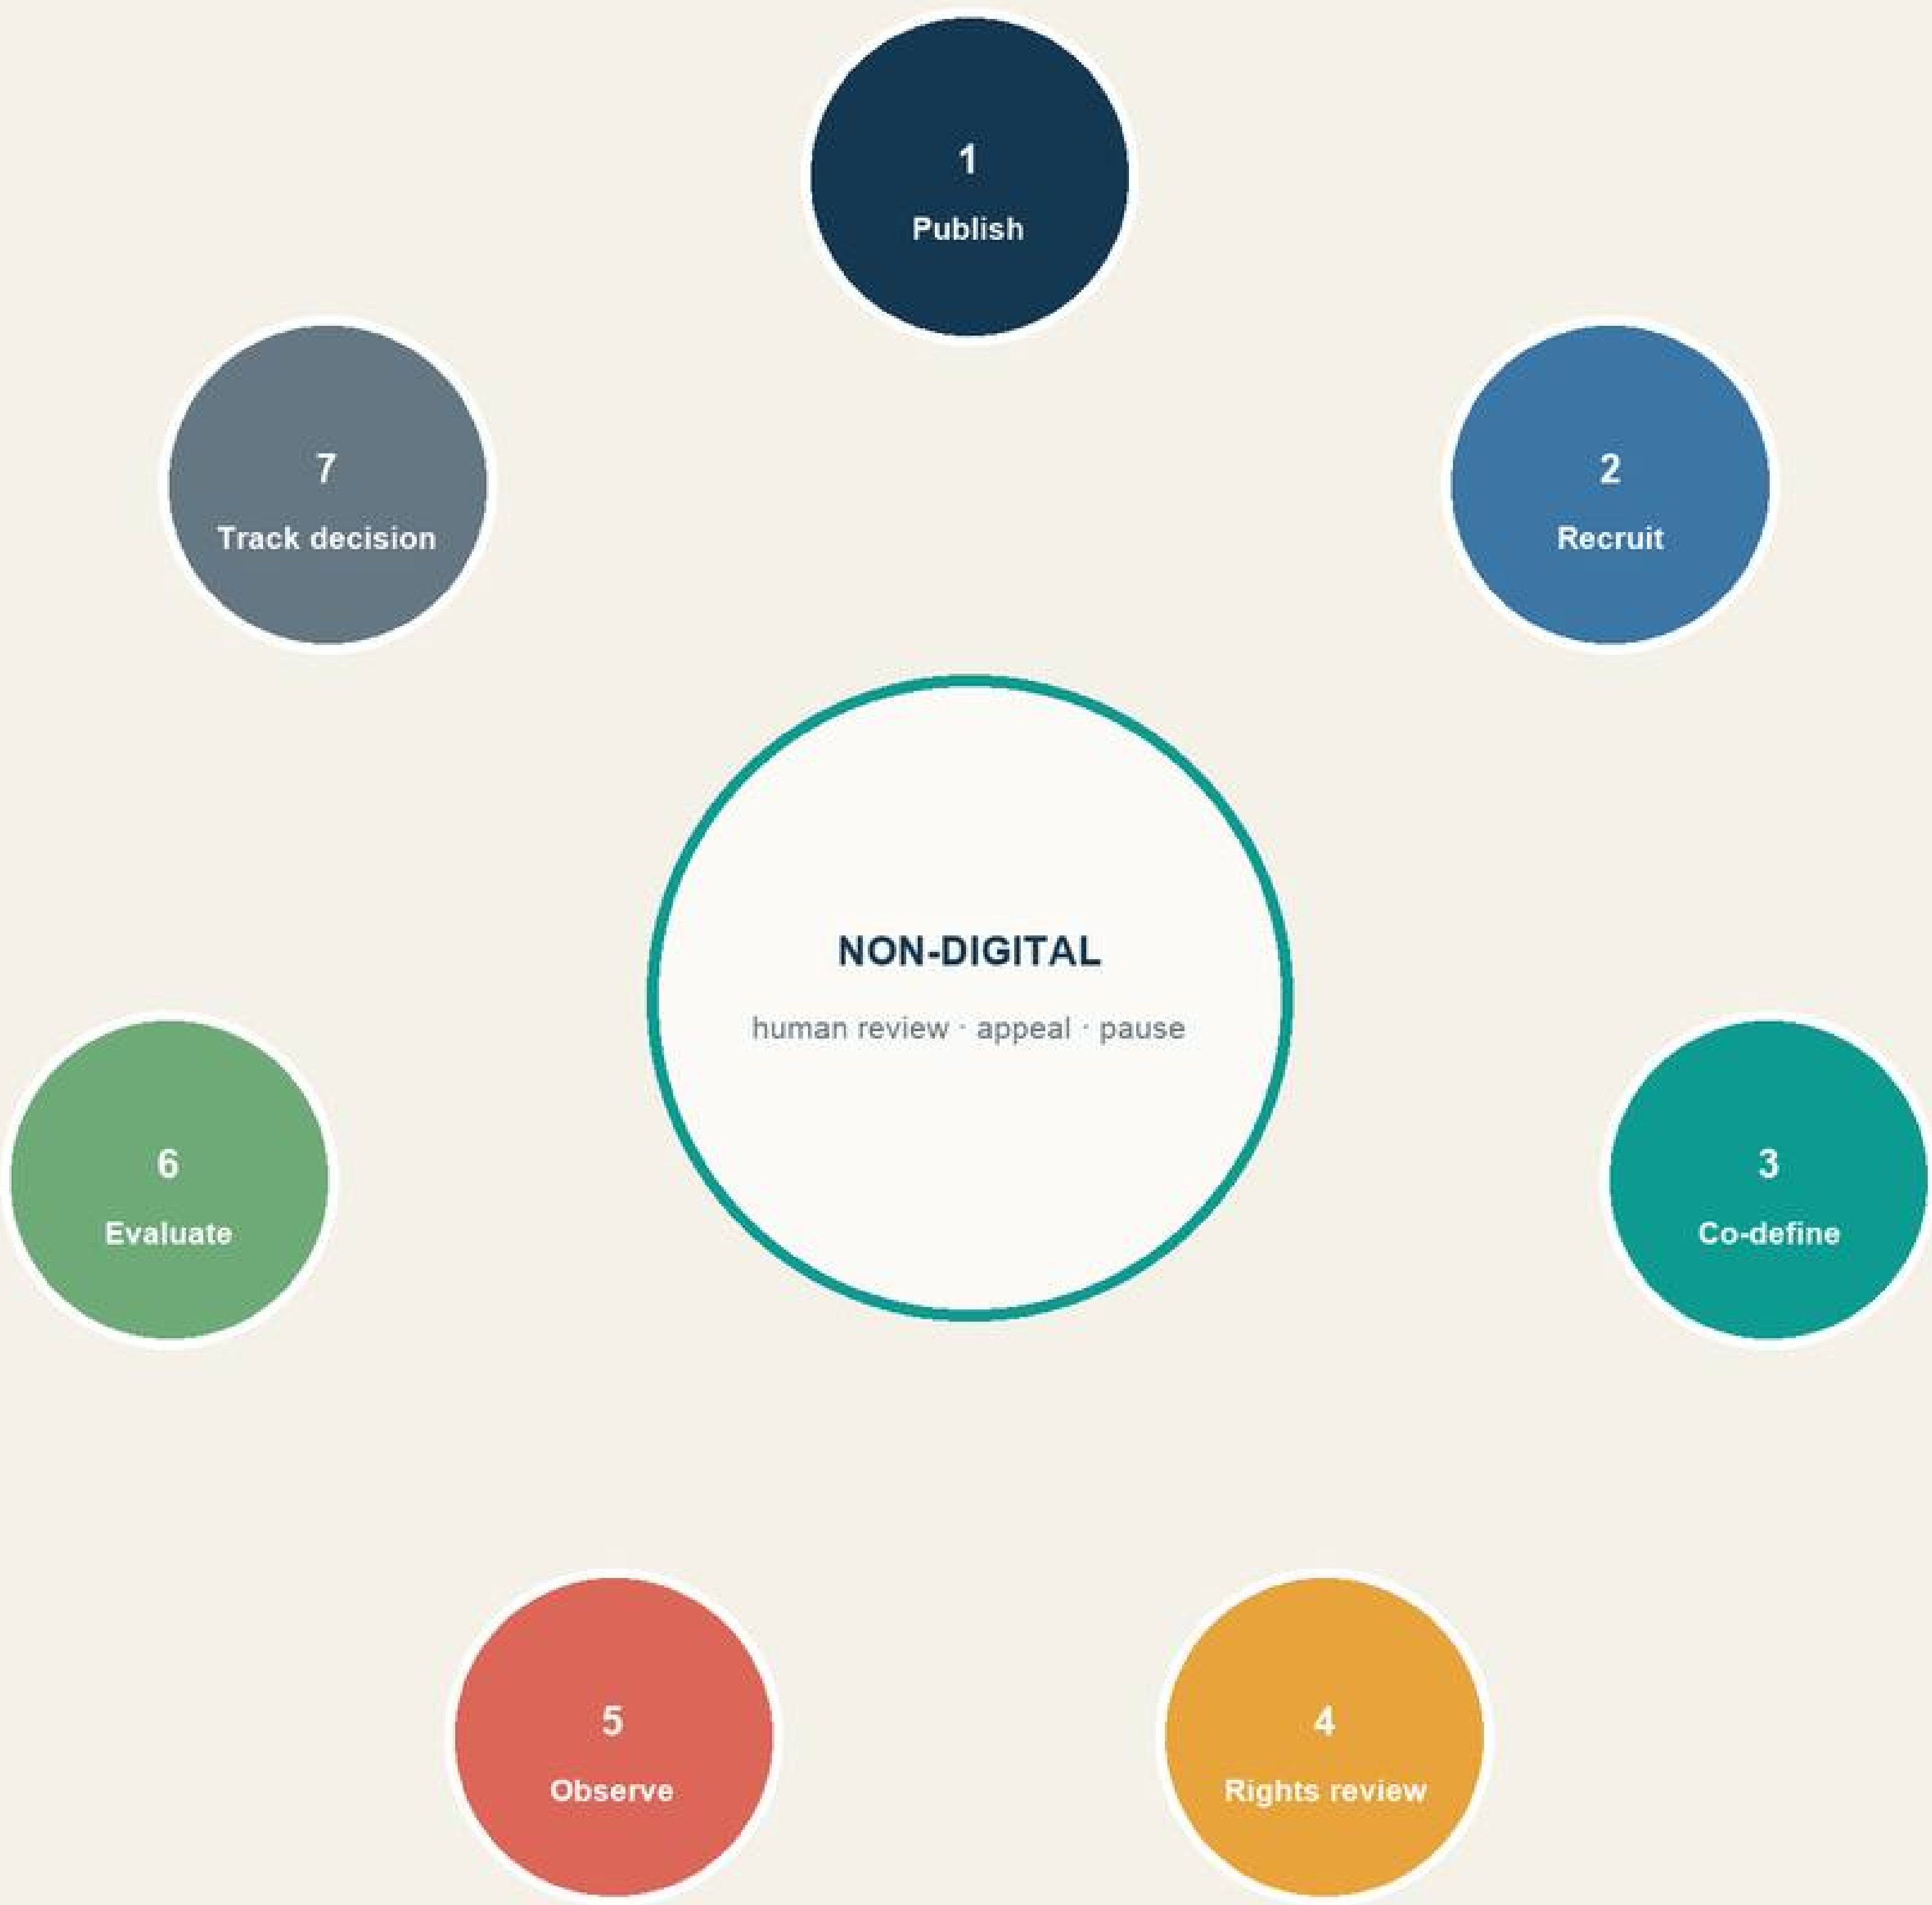

Targets enter formal performance documents only after baseline survey, professional review and confirmation by the lawfully determined responsible entities; they are not government commitments.

PROPOSED STARTING CONTROLS

Demand-brief completeness	≥95%
Public response rate	≥90%
High-risk takeover coverage	100%
Severe safety/privacy events	0
Critical accessibility barriers closed	100%
Exit completion	100%

MANDATORY PAUSE / EXIT TRIGGERS

- Demand owner or site rights unclear
- Unclear data provenance, version or legal basis
- No human fallback in a high-risk scenario
- Severe safety, privacy or fairness issue unresolved
- Whole-life cost or operations unaffordable
- No exit provision, deletion or alternative service

B01 / IDENTITY & LANDMARK KIT

RailWeave Identity System and Three Reversible Landmarks

Identity is built around project status, evidence and public service—not corporate logos, giant screens or permanent monuments.

RAILWEAVE



FIVE EVIDENCE COLOURS

L1

L2

L3

L4

L5

Tactile code | easy-read type | low-reflectance material | replaceable parts | low-glare night lighting

01

Validation Results Gallery




- pass/restrict/correct/stop
- model version + human review
- redacted summary

site, fire, maintenance and restoration to verify

02

Collaborative Innovation Courtyard

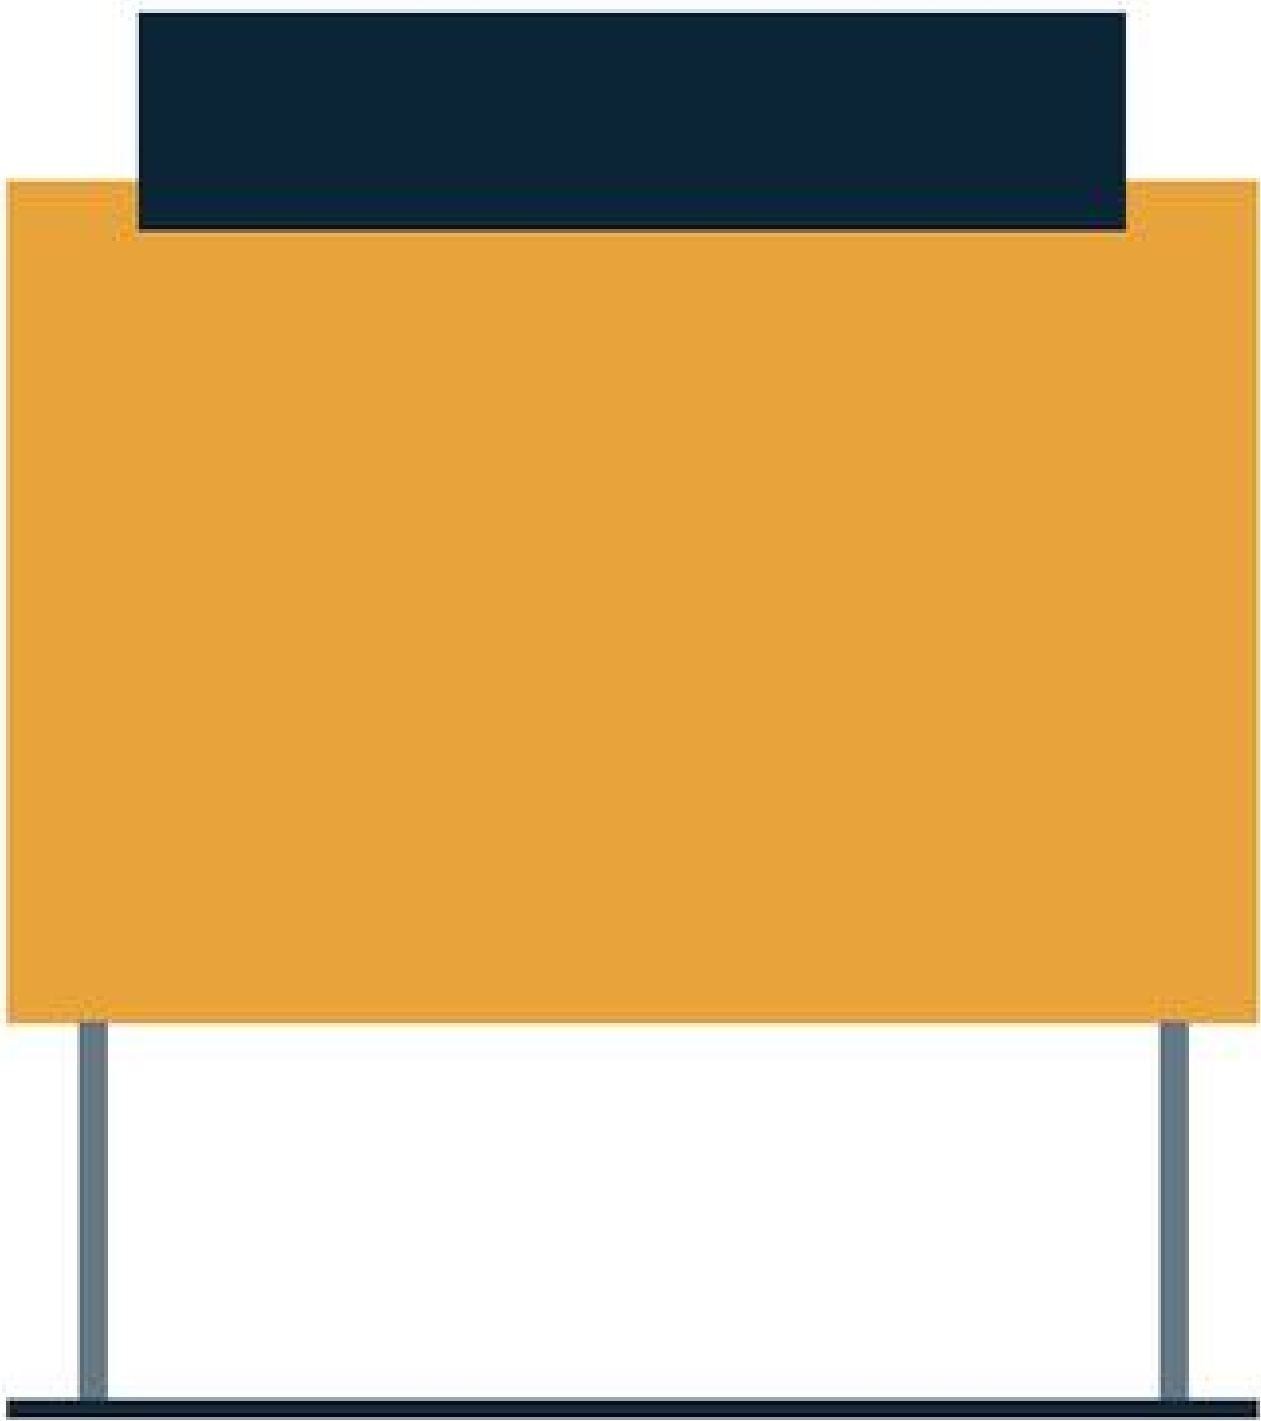


- paper/digital demand wall
- objection and exit record
- movable accessible parts

site, fire, maintenance and restoration to verify

03

First-Use Conversion Gateway

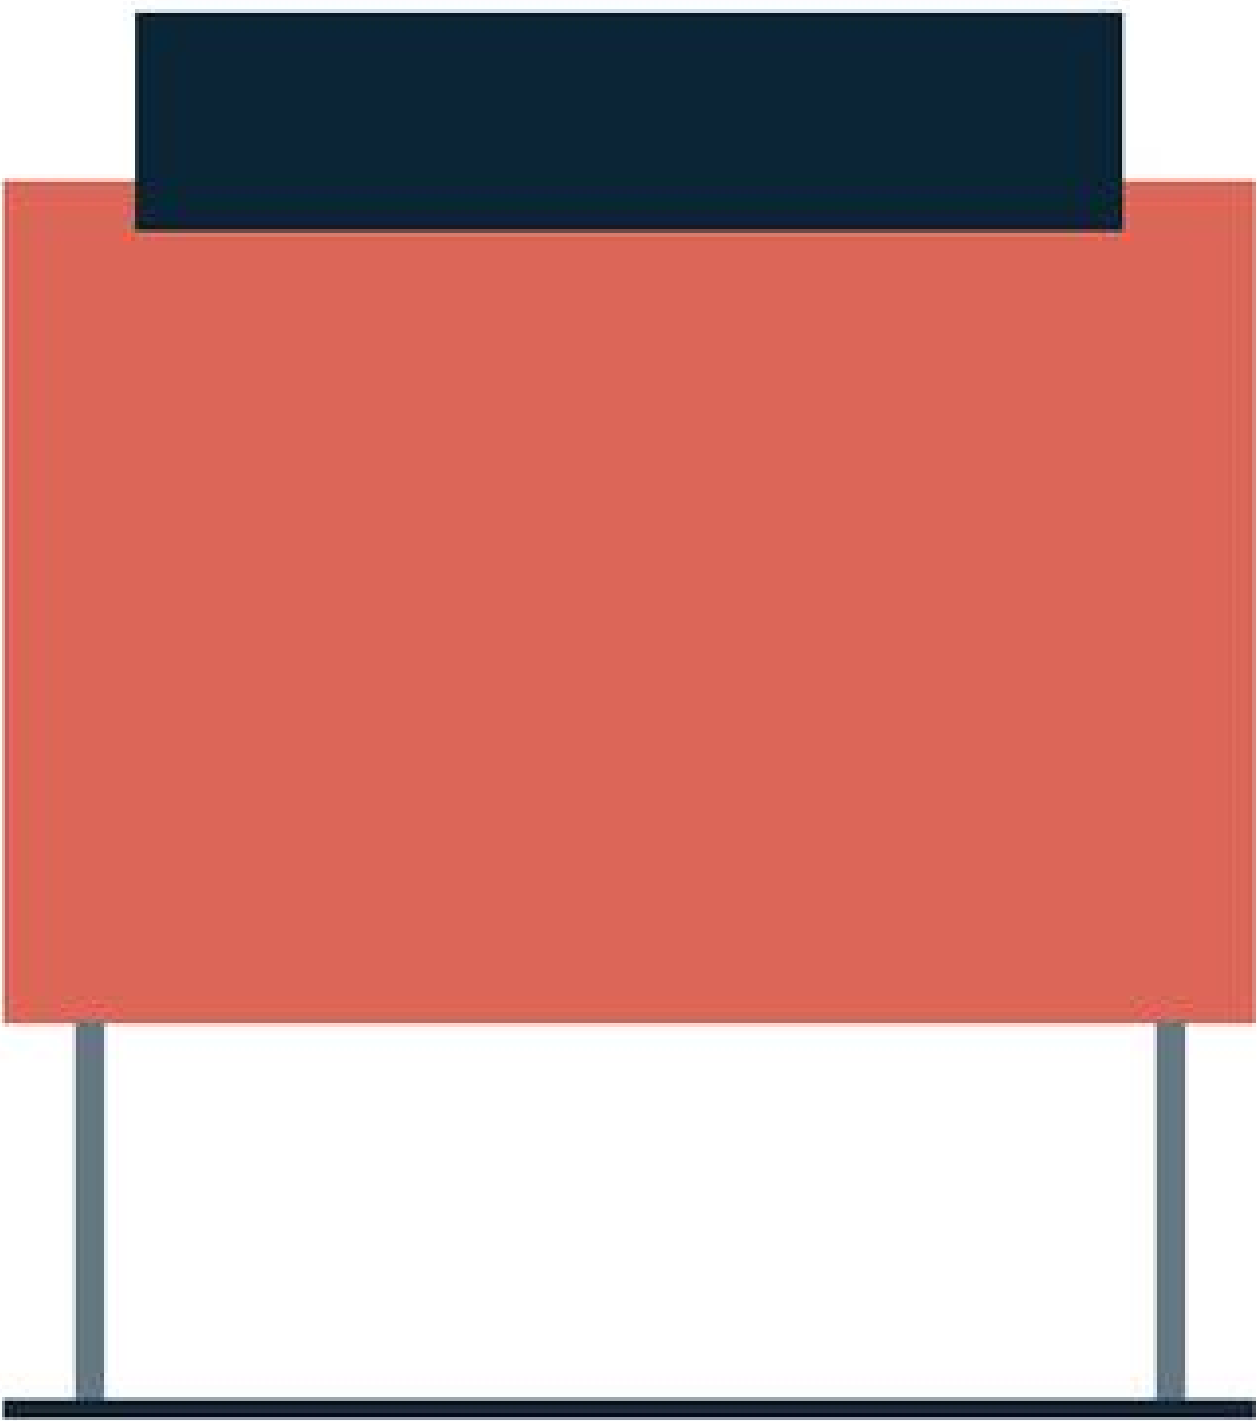

- demand-validation-procurement
- 90/180-day review
- rail mileage / project ID

site, fire, maintenance and restoration to verify
